

**CONFIDENTIAL**

911

~~SECRET~~

FILE: EB178 B-1  
Destructor Systems, Air Fed  
Incinerators  
5 July 1960

**MEMORANDUM FOR THE RECORD**

**SUBJECT: Installation of Model 2 Air-Fed Incinerator**

1. An idea has been generated by [redacted] for the testing and demonstration of the prototype Model 2 Air-Fed Incinerator. This idea is to actually install this incinerator in West Outbuilding.

25X1

2. A tentative location in Room 2D8B has been selected. [redacted] TSD/SEC, and [redacted] Office of Security/Safety, have concurred on the use of this room for the incinerator.

25X1

25X1

3. Pending approval of the use of Room 2D8B, the following steps would have to be undertaken:

a. 220 Volt, 3 phase, 60 cycle current would have to be brought into the room.

b. A hole approximately 10 inches in diameter will have to be cut in the wall to allow the stack to protrude through.

c. A stack will have to be placed up alongside of the building with a small piece extending above the top of the building.

25X1



inc

OVERALL HT. 64"  
OUTSIDE DIA 24"

80 TO 130 LBS/HR BURNING RATE

9" DIA STACK

25 JULY. UNIT WILL BE AVAILABLE


6 July 60 - [redacted] will determine what can be done.

~~SECRET~~

**CONFIDENTIAL**

25X1

CONFIDENTIAL

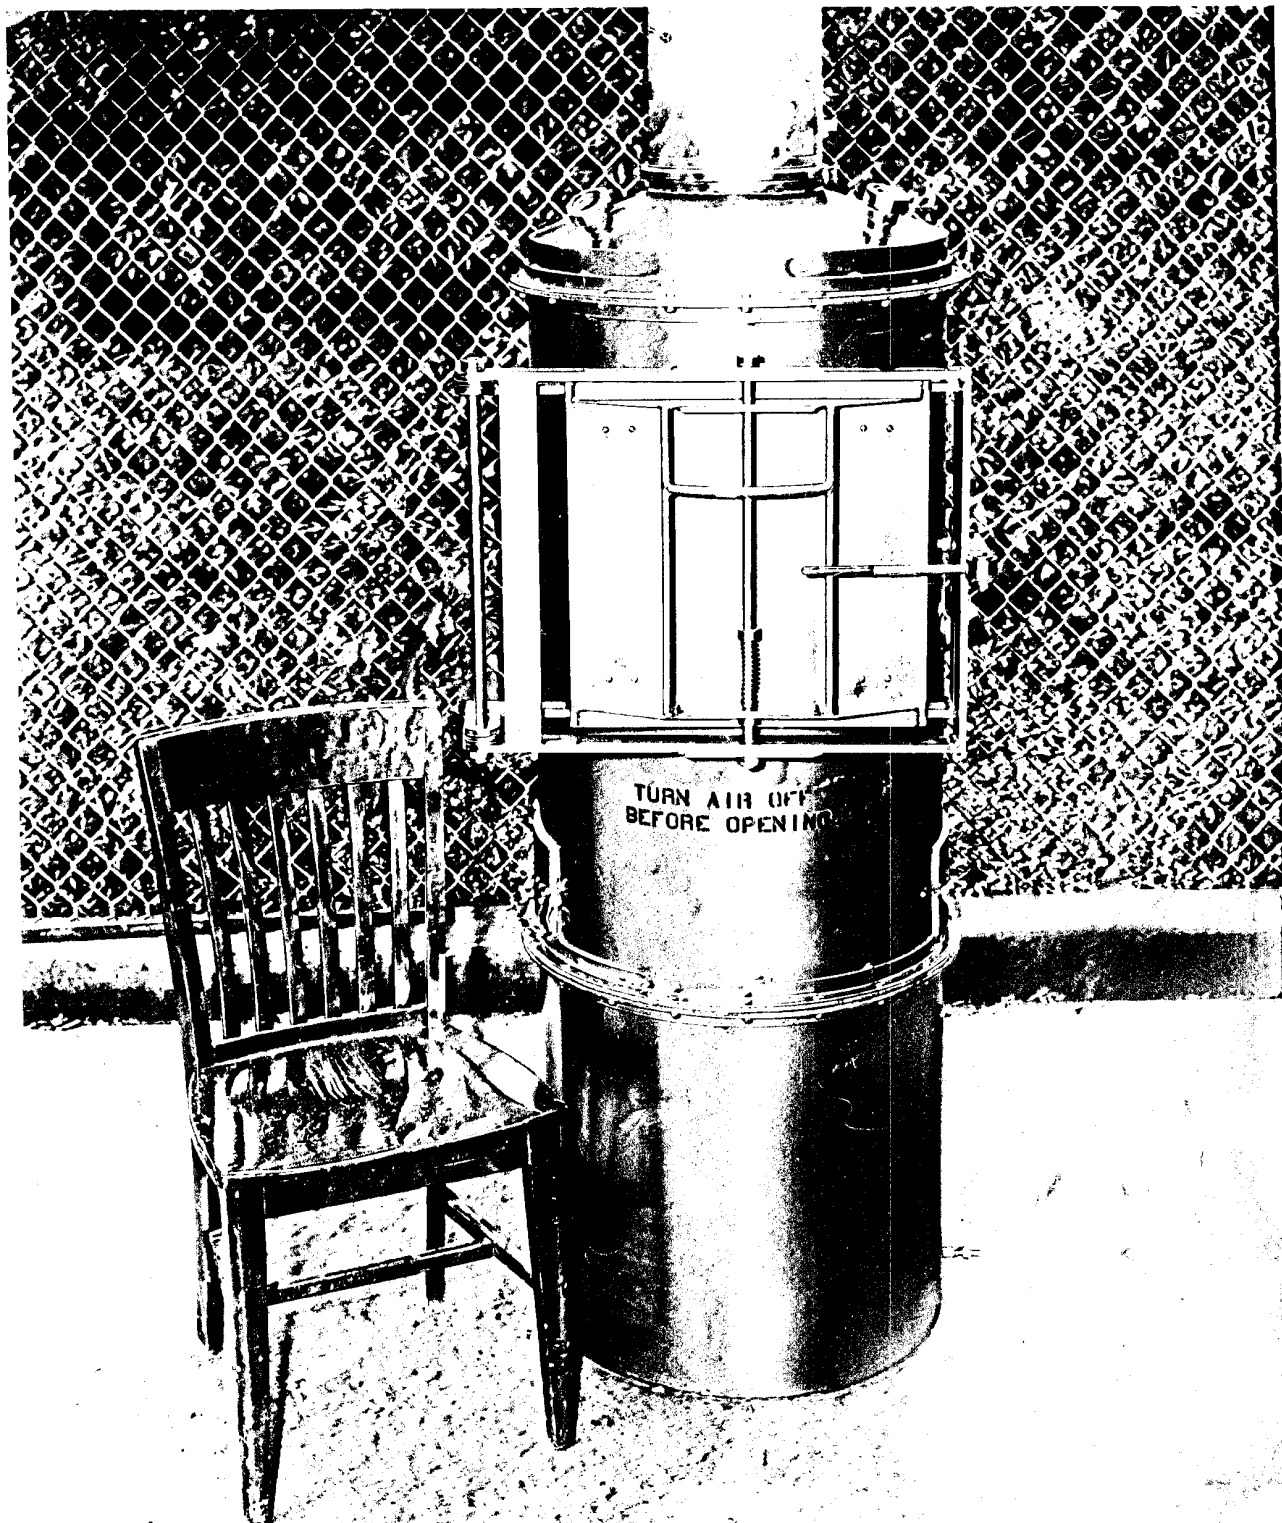

CONFIDENTIAL
