


**SECRET**


# INTEGRATED INFORMATION SYSTEM (IIS)

## DETAILED SYSTEM IMPLEMENTATION PLAN

Prepared for  
NATIONAL PHOTOGRAPHIC INTERPRETATION CENTER  
Second Report of Task Order No. 17



November 1, 1967



DECLASS REVIEW by NIMA/DOD

**SECRET**

GROUP 1: EXCLUDED FROM  
AUTOMATIC DOWNGRADING  
AND DECLASSIFICATION

WARNING

This document contains information affecting the national defense of the United States, within the meaning of Title 18, sections 793 and 794, of the U.S. Code, as amended. Its transmission or revelation of its contents to or receipt by an unauthorized person is prohibited by law.

Dec 15 2 32 PM '67  
STATE DEPT  
RECEIVED

SECRET

SCR 369

INTEGRATED INFORMATION SYSTEM (IIS)  
DETAILED SYSTEM IMPLEMENTATION PLAN

Prepared for  
NATIONAL PHOTOGRAPHIC INTERPRETATION CENTER

Second Report of Task Order No. 17



November 1, 1967



SECRET

**SECRET**

SCR 369

## TABLE OF CONTENTS

1. INTRODUCTION . . . . .	<u>Page</u> 1
2. PROGRAM MANAGEMENT . . . . .	2
2.1 Program Office Organization . . . . .	2
2.2 Program Office Functions. . . . .	2
2.2.1 Administration. . . . .	2
2.2.2 Operations. . . . .	10
2.2.3 Engineering . . . . .	15
3. SCHEDULES AND MANPOWER LOADINGS. . . . .	20
3.1 Software Development Schedule . . . . .	20
3.2 Hardware Procurement Schedule . . . . .	24
3.3 Training Schedule . . . . .	27
3.4 Test and Evaluation Schedule. . . . .	27
3.5 Documentation Schedule. . . . .	27
4. SYSTEM IMPLEMENTATION COSTS. . . . .	33
4.1 Program Office. . . . .	33
4.2 Acquisition of Software . . . . .	33
4.3 Acquisition of Hardware . . . . .	33
4.4 Data Base Development and Training. . . . .	35

APPENDIX

A Selection of IIS Implementation Plan . . . . .	A-1
B Implementation Requirements Planning Sheets. . . . .	B-1
C Application of CPM To IIS Scheduling . . . . .	C-1

**SECRET**

SECRET

SCR 369

## LIST OF TABLES

<u>Table</u>		<u>Page</u>
I	Implementation Responsibilities and Relationships . . . . .	4
II	IIS Implementation Cost Estimates . . . . .	34
III	IIS New Equipment Costs . . . . .	36

## LIST OF FIGURES

<u>Figure</u>		<u>Page</u>
1	Program Office Organization . . . . .	3
2	Prerequisites for the Implementation of IIS Capabilities. .	21
3	Software Development Schedule . . . . .	23
4	Basic Procurement Cycle . . . . .	25
5	Hardware Procurement Schedule . . . . .	26
6	Basic Training Cycle. . . . .	28
7	Training Schedule . . . . .	29
8	Basic Test and Evaluation Cycle . . . . .	30
9	Test and Evaluation Schedule. . . . .	31
10	Documentation Schedule. . . . .	32

SECRET

1. INTRODUCTION

25X1A This report is submitted in fulfillment of Task A.(4) of the Statement of Work under [ ] Task Order No. 17, to provide a detailed system implementation plan for the Integrated Information System (IIS).

The plan which is described herein was selected from a number of alternative plans in order to meet the requirement for establishment of a National Data Base in approximately one year and to provide for a concurrent initial operational capability which would include as many of the features of the IIS as were deemed necessary and practical under budgetary constraints. Accordingly, the plan provides for a National Data Base, and capabilities for data entry, verifying, editing, approval, data base update, query, Presentation sheet generation and report generation within 14 months. The remaining capabilities of target prediction, scheduling, COINS interface, cables, and on-line support to 3rd phase reporting will be provided within an additional 9 months.

The detailed plan as presented in the following sections includes a description of program management, its organization, planning and implementation responsibilities (Section 2), implementation schedules and manpower requirements (Section 3), and implementation costs (Section 4). Appendices A, B, and C are concerned respectively with the selection of the implementation plan to be detailed, detailed data utilized in deriving schedules and a critical path analysis.

SECRET

SCR 369

## 2. PROGRAM MANAGEMENT

Management of the IIS program will require the coordination and control of activities jointly involving contractor personnel and personnel from several divisions of the Center. It is therefore essential for the orderly development of the IIS that an organization be established with clearly defined responsibilities and authority to manage the implementation of the IIS. A Program Office is proposed for this purpose which can be staffed, either by Center personnel, by contractor personnel, or both. In defining the responsibilities of the Program Office, we have assumed that some equipment will be procured under contract as opposed to entirely GFE, some software will be developed under contract rather than developed entirely by the Center, and that services in support of training and other functions may be acquired under contract.

### 2.1 Program Office Organization

A Program Office consisting of a Program Manager and three functional areas for Administration, Operations, and Engineering is recommended as shown in Figure 1. Administration is a staff function, and Operations and Engineering are line functions. The operations functions are connected by a dashed line since it is deemed highly desirable that these functions be staffed by Center operational personnel even if program management is accomplished with contractor assistance.

### 2.2 Program Office Functions

The function of each area within the Program Office is described in terms of its planning and implementation responsibilities. The planning responsibilities are concerned with the preparation of specific plans. All plans are identified, but it should be noted that many of the procedures called for in these plans now exist at the Center. A determination as to which of the Center procedures to use and which to prepare will depend on Center policies and assignment of management responsibility for program office functions. Where plans must be prepared, work must be initiated immediately upon start of the implementation phase of the IIS program. The implementation responsibilities are concerned with execution of the plans. Since implementation actions may involve the participation of several functional areas, a summary of responsibilities by functional area and their interrelation for implementation actions is shown in Table I.

#### 2.2.1 Administration

The responsibilities in this area include program control, status reporting, configuration control, procurement, reliability and maintainability control, facility modifications and use of Center equipment for IIS development.

SECRET

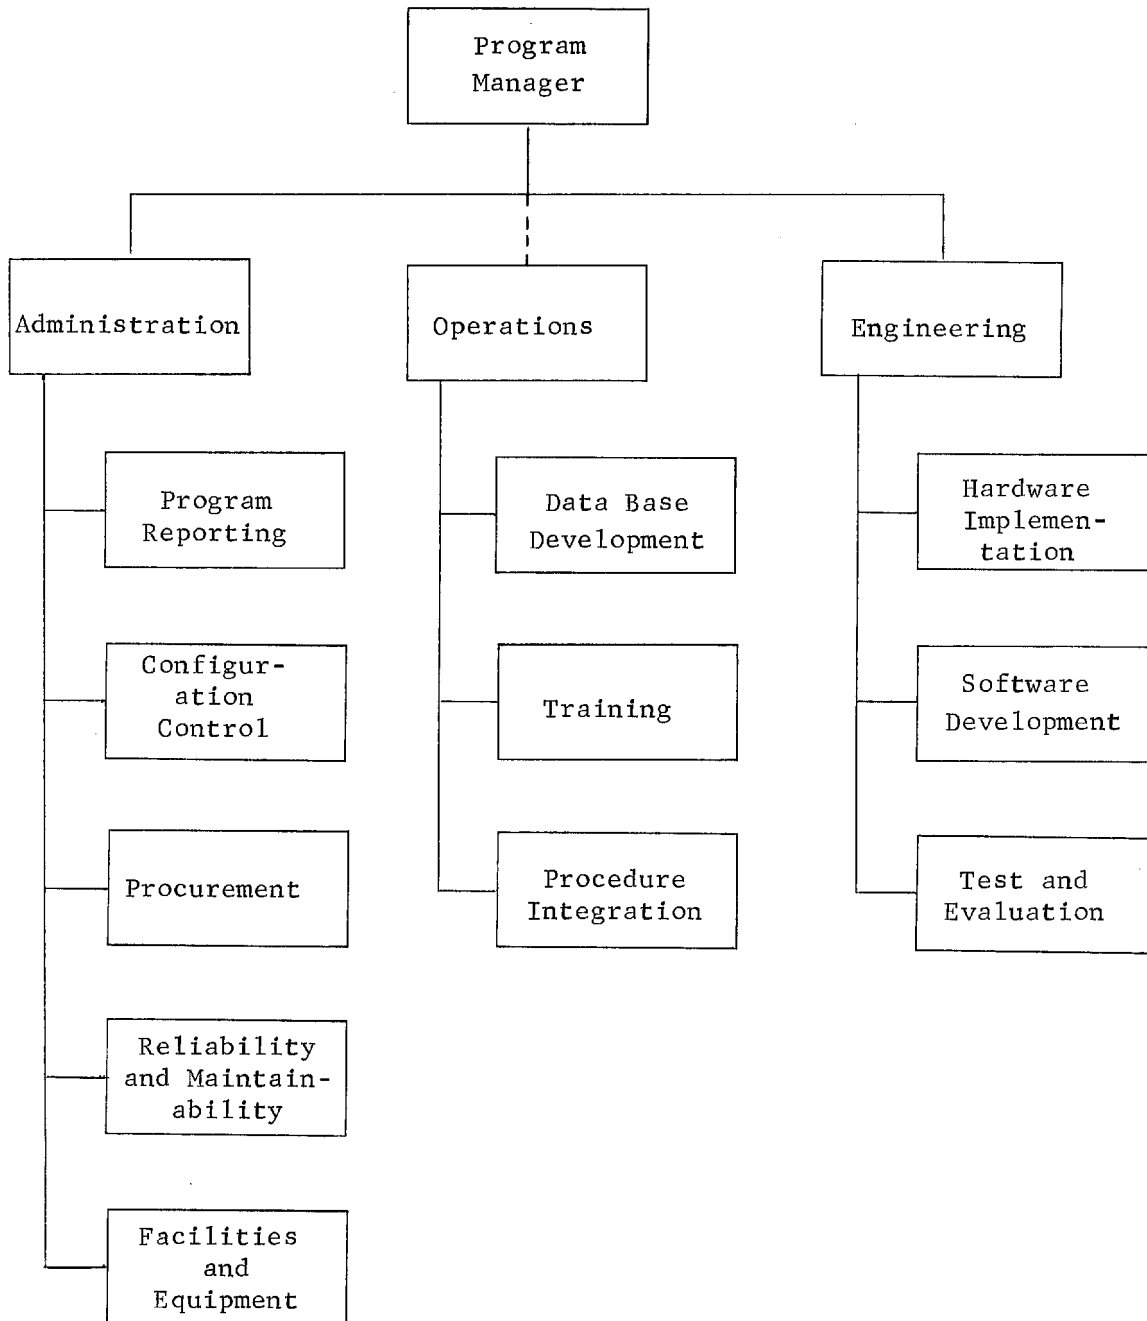


Figure 1 Program Office Organization



TABLE I  
IMPLEMENTATION RESPONSIBILITIES AND RELATIONSHIPS

FUNCTION  IMPLEMENTATION ACTION	ADMINISTRATION					ENGINEERING				OPERATIONS				
	Program Reporting	Procurement	Configuration Control	Facilities and Equipment	Reliability and Maintainability	Supervision	Hardware Implementation	Software Development	Test and Evaluation	Supervision	Data Base Development	Training	Procedures Integration	Contractor and In-house Efforts
GENERAL IMPLEMENTATION RESPONSIBILITIES														
Component Acquisition	Cost and Status Report's	Contract Support	System Design Control	Modification and Use	R&M Monitoring	Coordination	Hardware Monitoring	Software Monitoring	Quality Assurance	Coordination	DB Conversion	Conduct of Training		Component Production
System Conversion	Cost and Status Report's					Component Acceptance				Support Acceptance	DB Acceptance	Training Completion	IIS Capability Use	
Cost/Benefit Analysis	Analysis		Cost Recording										Benefit Recording	
SPECIFIC IMPLEMENTATION RESPONSIBILITIES														
<u>CONTRACT AND IN-HOUSE SUPPORT</u>														
Specifications Release			Release		Approval	Approval				Approval				
RFP Preparation (Contract Only)		Selection of Vendors				Coordination				Coordination				
Proposal Evaluation (Contract Only)		Contractor Selection				Technical Review				Technical Review				
Performance Monitoring	System Cost and Progress		Production Progress	Hardware Installation	R&M Attainment		Hardware Production	Software Production			DB Conversion	Training		
Contractor and In-house Effort Support		Administrative Support	Spares R'gmt. Eval.	Use of Center Equip.			Technical Support	Technical Support			Technical Support	Technical Support		
Component Acceptance					R&M Acceptance	Component Acceptance			Acceptance Testing	Service Prod. Acceptance				
Documentation Acceptance			Final											
<u>CHANGE CONTROL</u>														
Change Proposals	Entry of External Policies		Impact Study Referral				Hardware Proposal Review	Software Proposal Review	Proposal Submission		Proposal Submission	Proposal Submission		Proposal Submission

Page 1 of 2

SECRET

SECRET

SCR 369

TABLE I (CON'T)  
IMPLEMENTATION RESPONSIBILITIES AND RELATIONSHIPS

TABLE 1 (CON'T)

IMPLEMENTATION RESPONSIBILITIES AND RELATIONSHIPS

FUNCTION IMPLEMENTATION ACTION	ADMINISTRATION					ENGINEERING				OPERATIONS				Contractor and In-house Efforts	
	Program Reporting	Procurement	Configuration Control	Facilities and Equipment	Reliability and Maintainability	Supervision	Hardware Implementation	Software Development	Test and Evaluation	Supervision	Data Base Development	Training	Procedures Integration		
SPECIFIC IMPLEMENTATION RESPONSIBILITIES (CON'T)															
Change Approval			Review Board Action	Installations Review	R&M Review		Hardware Impact Study	Software Impact Study		Operations Review					Change Incorporation
Change Integration			Change Recording	Plan Update		Reengineering Effort	Specification Update	Specification Update	Plan Update		Plan Update	Plan Update			
<u>TESTING</u>															
Test Procedures Development					Manual Backup Proc.	Eng. Approval	Input to Hardware Tests	Input to Software Tests	Cat. II and III Proc.	Operations Approval		Training Procedures			Cat. I Procedures
Category I Tests					Failure Analysis				Evaluation						Execution
Category II Tests					Failure Analysis				Execution and Eval.		Data for Use in Tests				
Category III Tests					Backup Test Eval.				Execution	Evaluation		Training Test Eval.			
<u>EQUIPMENT INSTALLATION AND USE OF CENTER EQUIPMENT</u>															
Facility Modification	Status Reporting				Scheduling and Follow Up		Request Submission		Request Submission			Request Submission	Request Submission	Request Submission	Request Submission
Use of Center Equipment					Coordination				Request Submission			Request Submission	Request Submission		Request Submission

Page 2 of 2

Page 2 of 2

SECRET

5

SECRET

SCR 369

SECRET

SCR 369

## 2.2.1.1 Program Reporting

Planning Responsibilities

The required IIS Implementation Schedule and Manpower Requirements plans have been completed and are presented in detail in Section 3 of this report.

Implementation Responsibilities

This functional area is responsible for providing status reports on the overall IIS implementation, manpower utilization, contractor progress, program costs, and other data of management interest for control purposes.

The Critical Path Method (CPM), as used in the Center, is the management technique employed for planning and scheduling. Its employment for monitoring the IIS or modification of implementation plans or schedules as the result of approved configuration changes, revised funding, manpower availability, or policy decisions will be the responsibility of this functional area.

It is recommended that this area be responsible for a task to assemble cost/effectiveness data during final stages of IIS implementation and to compare this data with cost/effectiveness data of the current system, the extrapolated current system, and the present IIS design.

## 2.2.1.2 Configuration Control

"Configuration Management" is the management of technical requirements which define system equipment, software, products or services, and changes thereto. It is implemented through procedures by which uniform and mutually supporting methods for configuration identification, control and accounting are established and maintained for components of the system. The technical requirements include the requirements for engineering data, drawings, training and maintenance manuals pertinent to the system components.

Planning Responsibilities

A detailed set of Program Office procedures should be developed by this function to prescribe methods of component identification (numbers), control of change to the IIS baseline configuration during implementation, and configuration reporting and accounting. Required forms should be designed and made available for use.

SECRET

**SECRET**

SCR 369

Implementation Responsibilities

Throughout the implementation, this function should be responsible for:

1. Acquiring and analyzing information concerning the impact of a Change Proposal originating in one Program Office function on other activities.
2. Presenting Change Proposals and associated impact evaluations to a Change Control Board for approval.
3. Ensuring that appropriate changes are incorporated in related efforts when a Change Proposal is approved.
4. Verifying change implementation.
5. Maintaining an updated record of current configuration status and records concerning approved changes to the baseline configuration.
6. Conducting First Article Configuration Inspections (FACI) to ensure that components and documentation are complete.
7. Maintaining records of tests and inspections of components.
8. Reporting on, and accounting for, configuration status.

#### 2.2.1.3 Procurement

It is held likely that the procurement of long-lead time equipment and contractor support in software development will be initiated within the Center prior to the formal establishment of an IIS Program Office. Under these circumstances, it may be expedient to continue this method of meeting Program Office procurement responsibilities. Nonetheless, to ensure that the procurement responsibilities are met, the responsibilities under this concept of a Program Office are defined below:

Planning Responsibilities

This function should initially investigate the availability of GFE and in-house capability to meet IIS requirements. When the requirements for contractor support have thus been defined, this function should be responsible for preparation of the technical portion of RFP's to solicit contractor bids, including a statement of constraints on the use of other

**SECRET**

SECRET

SCR 369

than Center facilities in testing. The technical portion of the RFP's will be based on information as released by the Configuration Control function.

#### Implementation Responsibilities

With the start of work on contract end items, the procurement function should provide contractors with the necessary forms and procedures to be employed in:

1. Submitting Change Proposals
2. Reporting compliance with approved changes.
3. Category I test reporting
4. Requests for facility modification
5. Requests for temporary use of Center facilities in testing.

This function will also be responsible for monitoring contractor progress to ensure timely delivery of contract end items and for administrative support to contractors in contract matters.

#### 2.2.1.4 Reliability and Maintainability

The reliability of the IIS will be achieved by a highly reliable set of automated procedures, where automation can be effectively employed, backed up by manual procedures. The Reliability and Maintainability function of the implementation Program Office thus becomes concerned with both the reliability and maintainability of equipment and software and the reliability of the backup procedures.

The reliability of the automation will be jointly determined by the reliability of the hardware and software. IIS hardware specifications establish the minimum MTBF's for equipment and the procedures by which each potential vendor must determine the reliability of each piece of equipment.

Equally important is the contribution that can be made to system reliability through the proper application of software redundancy and diagnostic routines. Certain of these techniques have been included in the IIS design to insure the integrity of the IIS data base and approval procedures, but their potential value in other areas will undoubtedly come to light as a result of software development and experience with testing and initial operation of the IIS. When recognized they should be evaluated and, if practical, incorporated.

Finally, some testing of manual backup procedures should be accomplished to insure their effectiveness.

SECRET

### Planning Responsibilities

A plan should be developed for monitoring and reporting adherence to, and improvement in, reliability and maintainability of the automated IIS procedures, and testing of manual backup procedures. The procedures for measuring reliability and maintainability of automated IIS procedures should be developed, and procedures to be employed in evaluating proposed software diagnostic subroutines should be described.

### Implementation Responsibilities

Throughout the implementation, this function will be responsible for:

1. Analysis of equipment failures to ensure the accuracy of vendor MTBF data.
2. Analysis of effects of possible equipment failures on system operation. All these effects should be categorized according to severity to govern consideration of remedial action.
3. Analysis of the feasibility and advisability of including additional software diagnostic subroutines.
4. Evaluation of proposed configuration changes from system reliability and maintainability standpoints.
5. Continuous analysis of the requirements for equipment spares.
6. Scheduling, coordinating and evaluating tests of critical backup procedures.
7. Reporting of reliability and maintainability achievement.

#### 2.2.1.5 Facilities and Equipment

It is essential that facility modifications be scheduled and effected in sufficient time to permit installation of equipment in accordance with plans for system implementation. These modifications may include wiring installation, relocation of partitions and existing equipment, and/or re-allotment of space. Existing procedures in arranging for the temporary use of Center equipment should be reviewed and, if necessary, revised to allow for IIS implementation requirements.

Complete identification of facility modification requirements may be delayed until initial procurement action is approved and the equipment complement to be installed is firm. Information concerning installation requirements (wiring, space, floor-loading) should be obtained in proposals or through early coordination with the selected vendor to permit facility modification planning.

SECRET

SCR 369

The configuration of the UNIVAC 494 computer may be so unique or security constraints so rigorous that some Category II testing (by the contractor) may have to be accomplished on the Center equipment. The procedures for initiating requests for the use of this equipment including any required forms, should be established for use in procurement activities.

#### Planning Responsibilities

Prior to, or in the early stages of IIS implementation, this function should:

1. Develop the procedures to be employed by contractors in requesting use of Center equipment for Category II tests.
2. Provide a description of the installations requirements data to be acquired from vendors of equipment.
3. Prepare a basic schedule for the modifications to facilities.
4. Provide a tentative schedule for the use of Center equipment by contractors for test purposes.
5. Arrange for the acquisition or temporary use of any equipment required in IIS training.

#### Implementation Responsibilities

During the implementation period, this function will monitor facility modifications and take any necessary action to insure facility readiness for installation of IIS equipment. On request from contractors or in support of in-house efforts, it will arrange for the use of Center equipment for test purposes.

#### 2.2.2 Operations

Within the Operations area of the Program Office there must be a supervisory function, a data base development function, a training function, and a procedures integration function. The supervisory function controls the activities of the other three, provides general coordination with Engineering and Administration and is specifically responsible for:

1. Determining in-house capability to handle manual data base conversion and training, and submitting recommendations for contract support in these areas.
2. Preparation of the technical requirements for RFP action to obtain contractor services.
3. Contractor proposal evaluation

SECRET

**SECRET**

SCR 369

4. Determining the type and number of Center personnel to be given additional IIS training, and the requirements for new skills.

#### 2.2.2.1 Data Base Development

In the implementation of the IIS, there is a requirement to convert historical data in the existing data base into the form required by the IIS. Certain data in current records can be automatically converted to IIS format. Other data, buried in free text in existing records, must be manually extracted, reformatted, abstracted (in certain cases), and then entered into the IIS to make it available, on a selective basis, in response to queries and for use in reports and Presentations.

The selection of data to be converted by manual techniques is a Center decision. This decision must involve consideration of the length of the records to be maintained in the data base, the parameters to be converted, and the cost/benefits of a conversion. It is also expected that decisions as to the degree of conversion may be affected by deliberations on the national level.

For the purpose of this plan, it is assumed that desired portions of each unit record which cannot be automatically converted will be converted manually under plans and procedures generated by the Data Base Development function.

#### Planning Responsibilities

The Data Base Development function should prepare a time-phased plan for data base conversion. This plan should include:

1. A listing of the items in the records to be automatically converted, the current file format, and the IIS file format. (Provided to engineering)
2. A listing of the items to be manually converted, the current file format, and the IIS format.
3. Establishment of standardized terms and codes to be utilized in IIS files.
4. The proposed period for completion of manual conversion and the estimated manpower requirements.
5. A schedule for the conversion of records to coincide with implementation plans for IIS capability implementation.

**SECRET**



SECRET

SCR 369

6. A rationale for the removal of historical data from drum to tape (and to hard copy, if applicable) storage. This should be specified by record class and file sector.
7. Milestones in the data base development program for the creation and use of additional files.

#### Implementation Responsibilities

The primary concern of the Data Base Development function during implementation will be the actual conversion of the existing data base. However, it will additionally be responsible for:

1. Maintaining and updating the standards required to insure the integrity of the growing data base.
2. Developing methods of converting data from new sources to IIS format.
3. Preparing test data required by the test and evaluation function.
4. Interpreting higher echelon directives concerning reporting in terms of data base file structure requirements.
5. Reviewing change proposals which affect data base utility and providing a comprehensive analysis of effects on the current implementation program.
6. Coordinating with the development of software as required to handle revisions to data base conversion resulting from approved engineering changes.
7. Reporting of achievement in data base development.

#### 2.2.2.2 Training

New equipment and new procedures which are incorporated in IIS design will require training of Center personnel, and some personnel of external agencies, in the following areas:

1. Use of the new Presentation and Worksheets in reporting.
2. Use of the query console, including console operation and dialogue with the data base (extended to query stations in external agencies).

SECRET

3. Data entry.
4. Use of the VEA console.
5. Film control.
6. Data base maintenance (manual input).
7. Equipment maintenance and repair.
8. Manual back-up procedures.

The training programs should be geared to the provision of trained personnel required when a given IIS capability is implemented. Further, the programs should be developed for use in training new personnel subsequent to the implementation period. The training of external personnel may be accomplished through participation in Center programs or through external training programs, whichever is desirable.

#### Planning Responsibilities

A training plan should be prepared, supplemented by necessary training manuals, aids, and other material for each of the areas listed above. These plans should include a description of the IIS concepts involved, training schedules and tests, identification of critical training requirements, and the instructor, equipment and space requirements.

#### Implementation Responsibilities

In addition to the routine conduct of training and tests, this function will be responsible for:

1. Evaluating the impact of proposed engineering changes on current and completed training programs, including modifications and retraining requirements.
2. Proposing changes in IIS procedures where unanticipated human factors problems arise during training activities.
3. Modifying training programs as necessary to support approved design changes.
4. Monitoring the operational use of IIS procedures to determine training improvements and to update training manuals for future use.

SECRET

SCR 369

5. Coordinating training of external personnel.
6. Reporting training achievement.

#### 2.2.2.3 Procedures Integration

The IIS implementation plan introduces improved IIS capabilities into Center operation as soon as these capabilities are operational (Category III testing completed). At any point in the implementation period after the first IIS capability has been introduced, the Center will be operating with a mixture of IIS procedures and those employed previously. Integration of these procedures must be assured.

An additional integration problem lies in the fact that implementation of full IIS benefits may depend on manual data base conversion rates. While the IIS procedures can operate with that portion of the data base which can be converted to IIS format automatically, the full benefits of the query capability may have to await manual data conversion on a target by target, team by team, or some other expansion basis. Interim methods of operation, where the full IIS capability does not exist, should be developed.

#### Planning Responsibilities

While the major problems in procedures integration have been considered in developing the overall implementation plan, the procedural details of operation with a mixture of IIS and current procedures must be developed, including the requirements for temporary use of additional personnel, if any, during this operation. In addition, a method of recording statistical data which can be analyzed to determine the actual benefits of IIS procedures should be developed.

#### Implementation Responsibilities

During the implementation period, the Procedures Integration function should monitor the implementation and expansion of IIS capabilities and should additionally:

1. Monitor system operation with current procedures to develop statistical data on throughput, times, manpower utilization, and other factors for Center activities in which IIS procedures will be employed.
2. Monitor system operation in activities in which IIS procedures have replaced other procedures to acquire statistical data for comparison with that developed in 1, above and to assure that the operational IIS satisfies the Center requirements.

SECRET

**SECRET**

SCR 369

3. Modify the procedures integration plan in accordance with approved engineering changes and any resulting changes in Data Base Development and Training plans.
4. Provide progress reports on IIS implementation reporting any areas where operational deficiencies are noted.
5. Provide a final report on benefits of the implementation.

#### 2.2.3 Engineering

The Program Office functions in this area include a supervisory function, a hardware implementation function, a software development function, and a test and evaluation function. The supervisory function controls the activities of the other three, coordinates with Operations and Administration, and is specifically responsible for:

1. Determining in-house capability for software development and recommending the level of contract assistance to be procured.
2. Technical approval of hardware and software specifications.
3. Review of contractor proposals to provide hardware or software and make recommendations for vendor/equipment selection.
4. Technical acceptance of IIS engineering components.

##### 2.2.3.1 Hardware Implementation

The hardware in the IIS design consists of the central processor, peripheral equipment, and a number of remote consoles and data entry devices. The central processor and peripheral equipment employed in current processing will be employed in IIS operations although some augmentation will be required. However, equipment which will be identical to that in current inventory is assumed to be subject only to acceptance testing, while the remote consoles and data entry devices will be subject to standard engineering procurement procedures. The Hardware Implementation function will, under the above constraint, be responsible for the adequacy of the hardware components.

#### Planning Responsibilities

The Hardware Implementation function will be governed by the general implementation plan and the plans for equipment testing developed by the Test and Evaluation function.

**SECRET**

SECRET

SCR 369

Implementation Responsibilities

This function will be responsible for:

1. Technical assistance to equipment vendors.
2. Monitoring of vendor performance in provision of IIS equipment including central processor and peripheral augmentation components.
3. Review and approval of engineering change proposals submitted by equipment contractors.
4. Determining the impact of change proposals initiated by other functions on the acquisition of IIS hardware.
5. Assistance to the Configuration Control function in First Article Configuration Inspections (FACI).
6. Submitting recommendations for acceptance of equipment components.
7. Provision of installation requirements involving modification of facilities to the Facilities and Equipment function.
8. Reporting on equipment acquisition.

2.2.3.2 Software Development

A high degree of coordination must be maintained in the development of IIS software packages to ensure compatibility in the operational support which they provide. In addition, in the phased implementation of individual IIS capabilities, portions of a particular program package may be operationally required much sooner than other portions of the same package. The Software Development function will provide this coordination.

A requirement will also exist for IIS design modification to accommodate optional methods of coding software packages and modifications to system requirements. The Software Development function should be staffed to provide these interpretations in any software area.

Planning Responsibilities

The Software Development function will operate under the provisions of the general implementation plan and the plans for testing produced by the Test and Evaluation function. There is no requirement for production

SECRET

of a special plan for this function. A limited amount of planning activity will be required in the provision of input to plans generated by other functions.

#### Implementation Responsibilities

This function will be responsible for:

1. Technical assistance to contractors, including modification of the IIS design concepts.
2. Review and approval of change proposals submitted by software developers (in-house or contractors).
3. Determining the impact of change proposals initiated by other functions on the software development program .
4. Verifying that appropriate changes in software are effected in support of approved changes in the IIS design.
5. Arranging for the use of Center facilities when required for software checkout and test.
6. Submitting recommendations for software acceptance.
7. Reporting achievement in the development of software.

#### 2.2.3.3 Test and Evaluation

The IIS design includes an intricate combination of hardware and software operating on an extensive, structured, data base. It is essential that tests be conducted prior to operational use of components in routine system operation to ensure:

1. Compliance with specifications for production of end items.
2. Compatibility in interactions with other components.
3. Performance in providing a system capability which can be effectively employed by Center personnel.

The three levels of testing described above are designated Category I, II and III tests, respectively. Category I tests will be performed by

SECRET

SCR 369

contractors or the in-house effort charged with production of the end item. Category II tests will be directed and evaluated by the Test and Evaluation function. Category III tests will be executed by this function, but results will be evaluated by the Operations function. The Test and Evaluation function will nevertheless be responsible for establishing test objectives, procedures, and reporting requirements and for analysis of test results.

#### Planning Responsibilities

As an initial implementation effort, the Test and Evaluation function should prepare:

1. The overall test plan describing:
  - a. Hardware to be tested
  - b. Software to be tested
  - c. Test schedules
  - d. Test objectives, where applicable, for reliability, maintainability, quality, compatibility and human factors.
  - e. Required test environments.
  - f. Test plan approval procedures
  - g. Test reporting
  - h. Acceptance procedures
2. A detailed description of test data required in Category II and III tests (for submission to Data Base Development function).
3. A schedule of requirements for the use of Center equipment in testing (for submission to the Facilities and Equipment function).

#### Implementation Responsibilities

During implementation, this function will be responsible for:

1. Preparation of test procedures for each of the scheduled tests. These procedures should detail any simulations to be employed in lieu of actual operation.
2. Modifying test procedures to conform to approved engineering changes.

SECRET

SECRET

SR 369

3. Monitoring Category I tests performed by contractors or in-house evaluating results, and reporting on conformance with component specifications.
4. Executing Category II tests, evaluating results, and submitting engineering change proposals as necessary.
5. Conducting Category III tests and summarizing test results for acceptance action.
6. Reporting test and evaluation achievement.

SECRET



SECRET

SCR 369

### 3. SCHEDULES AND MANPOWER LOADINGS

Discussions between NPIC and [ ] personnel concerning the various implementation plans outlined in Appendix A resulted in a decision to provide schedules and costs (including manpower loadings) for a system which would permit on-line access to the IDF and associated subfiles by intelligence community personnel, both inside and outside the Center, in approximately 14 months after the beginning of the major implementation effort. Capabilities of this First Operational Phase include real-time queries of the IDF, the use of the Presentations and Worksheets, and the automatic preparation of First and Second Phase Reports.

25X1A

The Prediction and Assignment functions to be used in the scheduling of First and Second Phase Readout and to assist in film distribution are added to create a Second Operational Phase. Automatic processes to aid in the production of Third Phase Detailed Reports and the equipment to support them are introduced to create the Third Operational Phase. As shown in Figure 2, certain tasks must be completed before others can be undertaken, and operational capabilities will become available only upon the completion of various sets of tasks. It should be noted that this figure shows only the prerequisites for the accomplishment of certain tests on the attainment of the various Operational Phases and the month (in circles on the diagram) after start of implementation when that task is to be complete. Details of the schedules and manpower loadings for their accomplishment are provided in the remainder of this report and its Appendices.

The implementation plan selected required approximately 36 people to prepare, test and document computer programs, and to assist in the conduct of Category III (Operational) Tests involving these programs. Staffing of the Program Office described in Section 2 of this report is subject to Center organization and policy, therefore, no manpower estimates for that activity have been included.

#### 3.1 Software Development Schedule

Figure 3 is a bar chart illustrating the level of effort (in numbers of people) required to develop and test the various computer program packages necessary for system operation.

The software development schedule provides for the creation of 13 program packages. Eleven of these packages correspond directly to eleven of the twelve software specifications provided by the contractor as part of the design documentation. The program package entitled "Miscellaneous Utility Programs" includes the specification for "Data Base Maintenance and Periodic Update" and additionally provides time and manpower to cover unforeseen contingencies in adapting programs to RUM System requirements.

SECRET

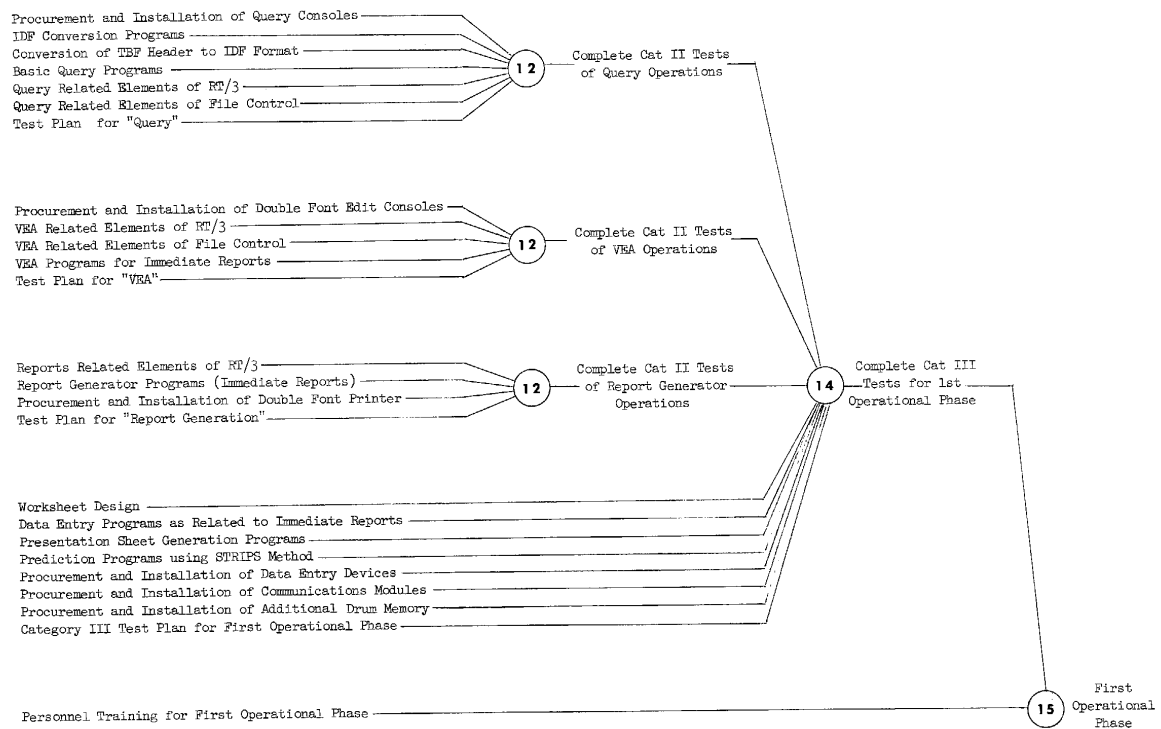


Figure 2 Prerequisites for the Implementation of IIS Capabilities (1 of 2)  
(First Operational Phase)

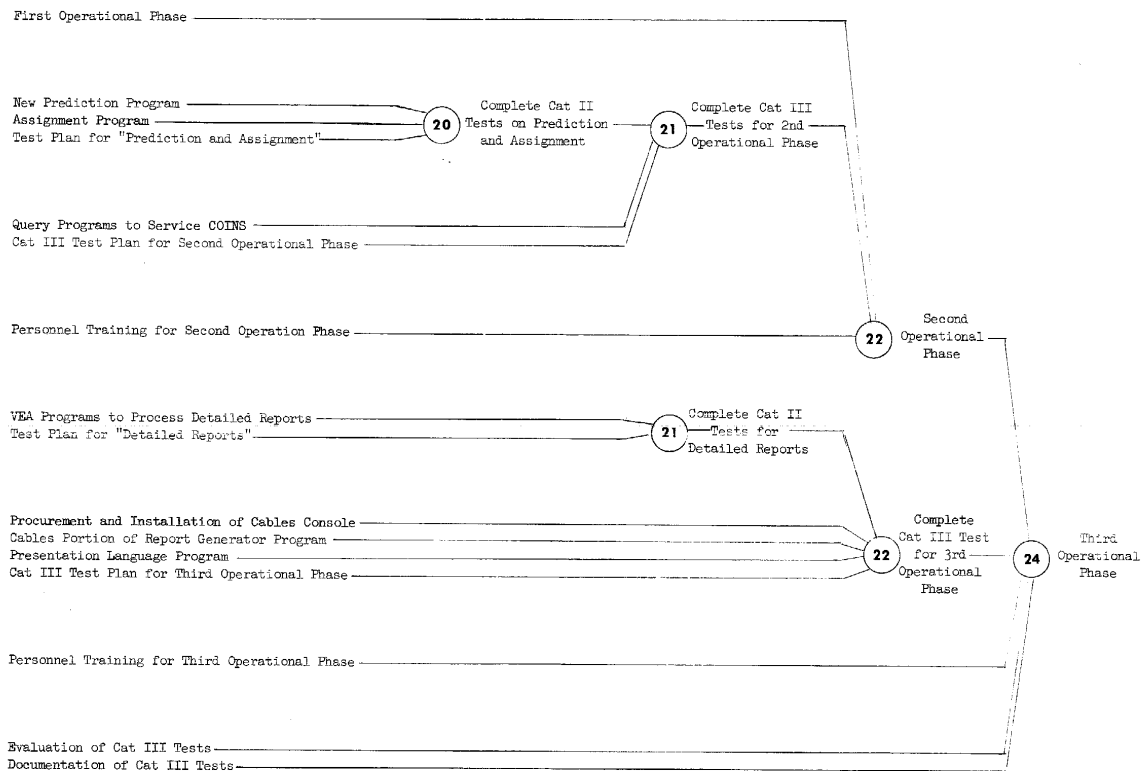


Figure 2 (Con't) Prerequisites for the Implementation of IIS Capabilities (2 of 2)  
(Second and Third Operational Phases)

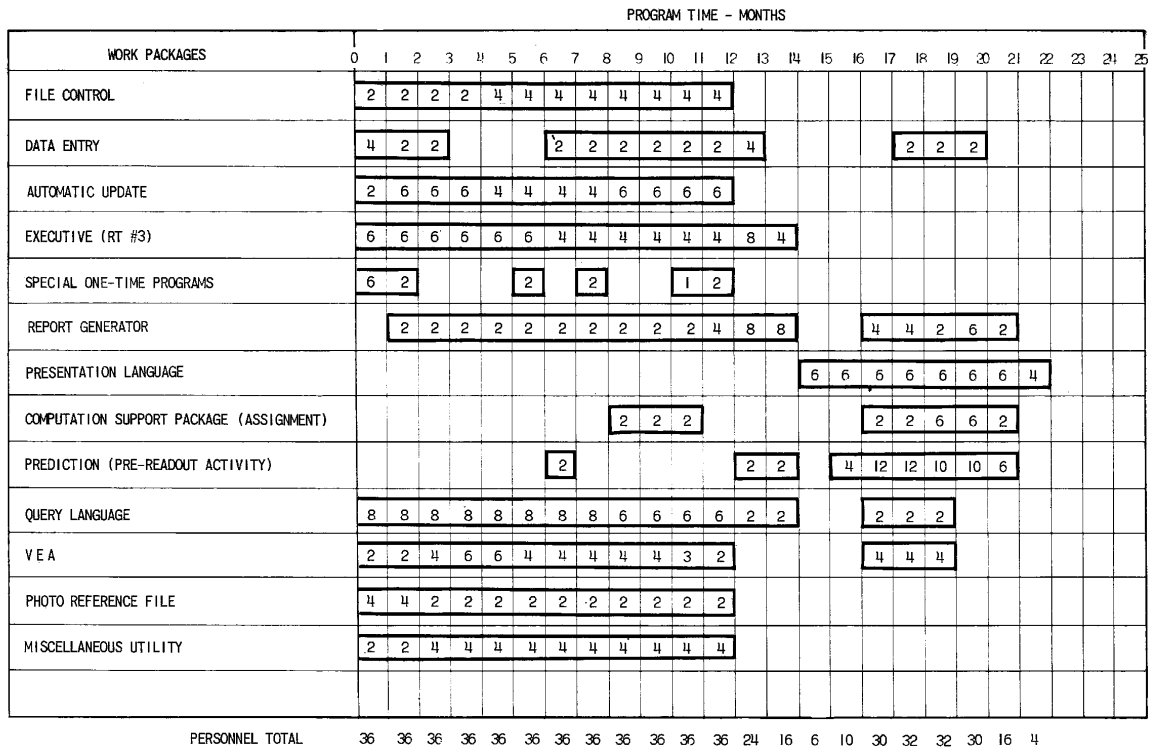


Figure 3 Software Development Schedule

SECRET

SCR 369

Additionally, we have provided manpower and time for the creation of special "One-Time" programs which may prove desirable in data base conversion and for similar purposes.

It will be noted that, in some cases, manpower is provided beyond the date when a program is scheduled for completion in Figure 2. This additional effort will be used to assist in the Category II and Category III testing which involves the particular program.

Some program packages are longitudinally divided. This division has been made to assist in maintaining a balanced work load and is feasible because some aspects of the programs are not required until the Second and Third Operational Phases.

Appendix B of this volume contains the set of Implementation Planning Sheets which further define the specific efforts undertaken in each program package. Relationships among the packages and their various segments are shown in the Arrow Diagram and CPM analysis in Appendix C.

### 3.2 Hardware Procurement Schedule


Figure 4 illustrates a basic procurement cycle which starts at the time of the approval and release of the specifications and ends at the completion of the Category II tests. The elapsed time interval between the signing of the contract and the delivering of the equipment is, of course, dependent upon the particular item that is being procured.

Figure 5 illustrates the application of this basic procurement cycle to the particular needs of the IIS Implementation Plan. The Hardware Procurement Schedule considers only those items of hardware which are not currently at the Center. It is the intent of the Implementation Plan to develop system capabilities as fully as possible, at the earliest possible date; the procurement schedule reflects this intent by scheduling delivery of all required hardware items of a given type at the same time.

The critical item for procurement is the Double Font Edit Console. If First Operational Phase capability is to be attained in 14 months, procurement of these devices must be initiated two months in advance of the start of other implementation activities.

It will also be noted on Figure 5 that no preliminary procurement cycle is provided for equipment directly available from UNIVAC for use with the central computer. It is assumed that the Center has a standard contract with this vendor and can place an order as soon as funds are available.

SECRET

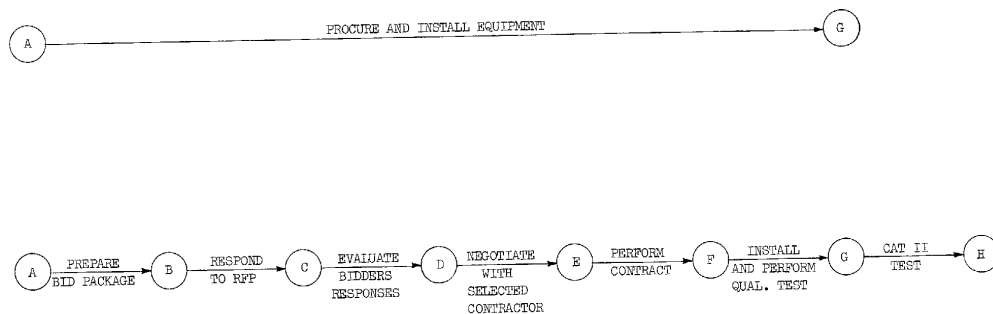

MILESTONES

- A -- RELEASE SPECS.
- B -- RELEASE BID PACKAGE
- C -- RECEIVE BIDS
- D -- WINNER SELECTED
- E -- CONTRACT SIGNED
- F -- EQUIPMENT DELIVERED
- G -- QUALIFICATION TEST COMPLETED
- H -- CATEGORY II TESTS COMPLETED

TIMING IN MONTHS	
TASK	TIME
A-B	1/2
B-C	1-1/2
C-D	1-1/2
D-E	1-1/2
E-F	VARIES
F-G	1
F-H	VARIES
A-G	VARIES

Figure 4 Basic Procurement Cycle

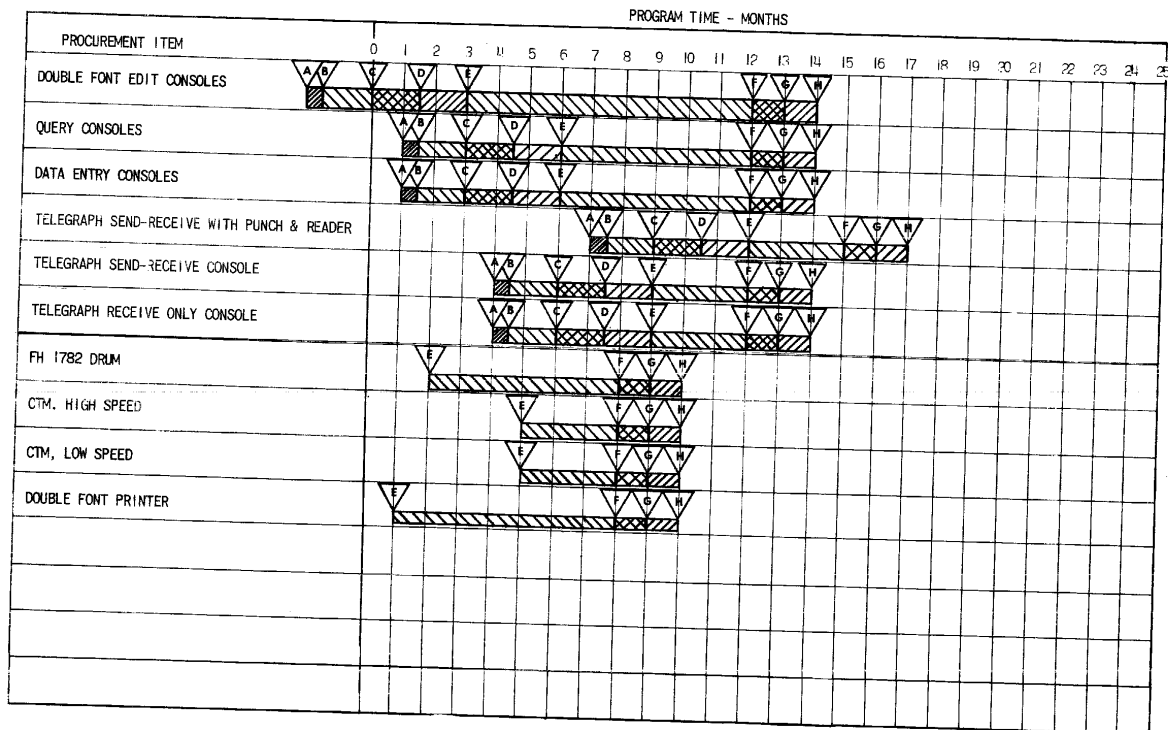


Figure 5 Hardware Procurement Schedule

SECRET

26

SECRET

SCR 369

**SECRET**

### 3.3 Training Schedule

Figures 6 and 7 illustrate a basic training cycle and a training schedule designed to meet the requirements of the implementation plan. The training program must be integrated with the normal work schedules of Center personnel and will be planned so as not to interfere with their normal duties.

### 3.4 Test and Evaluation Schedule

Figure 8 illustrates the basic events and milestones in a typical Test and Evaluation Cycle. Category I Tests are component tests and are performed by the component supplier. Category II Tests are subsystem tests and, in this Implementation Plan, evaluate the combinations of equipment, programs and files which jointly provide a specific capability (e.g., the ability to query the data base in real-time). Category III Tests are operational tests using Center personnel.

Figure 9 provides schedules for the preparation of test procedures and the conduct of tests in both Category II and Category III. Preparation of the plans is a Program Office function, therefore, no manpower loadings are provided. However, conduct of these tests will require support from programming personnel as indicated (in terms of numbers of people) on the diagram.

### 3.5 Documentation Schedule

Figure 10 provides schedules for the preparation of the final documentation of the capabilities tested in Category II and Category III tests. This documentation will be completed as specified in the technical requirements prepared by the Configuration Control function of the Program Office.

The estimated number of Center software development personnel that will be required to directly support the various documentation tasks are included within the bars for each month. The total number of Center software development personnel required in each month is shown as the bottom line of the chart.

**SECRET**





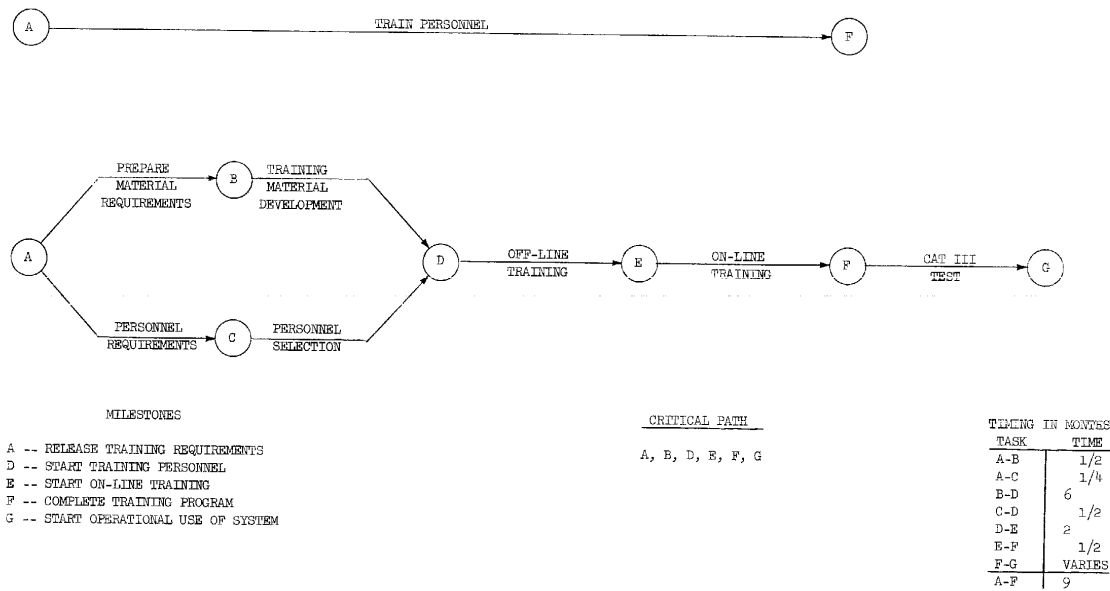


Figure 6 Basic Training Cycle



Approved For Release 2002/09/04 : CIA-RDP78B04747A001900050001-6

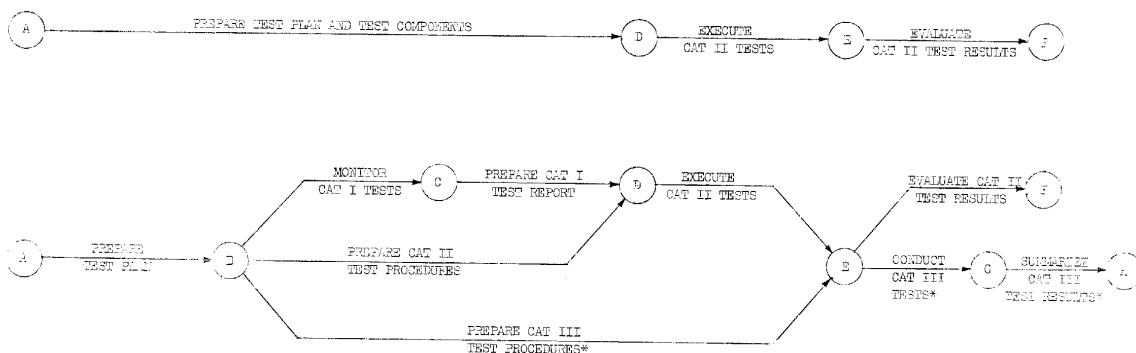

#### MILESTONES

- A -- RELEASE SPMS
- B -- OVERALL TEST PLAN PREPARED
- C -- CAT I TESTS COMPLETE
- D -- CAT II TESTS START\*
- E -- CAT III TESTS START\*
- F -- COMPONENT TEST PROGRAM COMPLETED
- G -- CAT III TESTS COMPLETED
- H -- TEST PROGRAM COMPLETED

\*These items shared with other components.

#### CRITICAL PATH

A, B, D

TIMING IN MONTHS	
TASK	TIME
A-B	3
B-C	2
B-D	6
B-E	VARIES
C-D	1/2
D-E	VARIES
E-F	VARIES
E-G	VARIES
E-H	VARIES
A-D	9

Figure 8 Basic Test and Evaluation Cycle

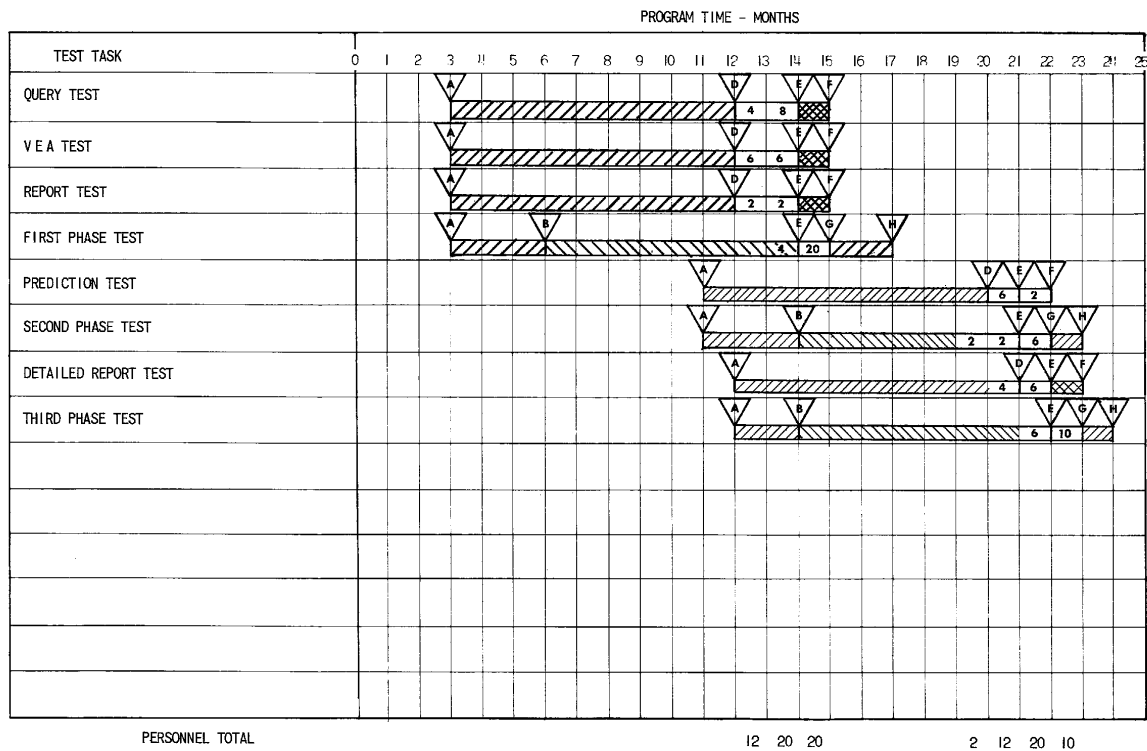


Figure 9 Test and Evaluation Schedule

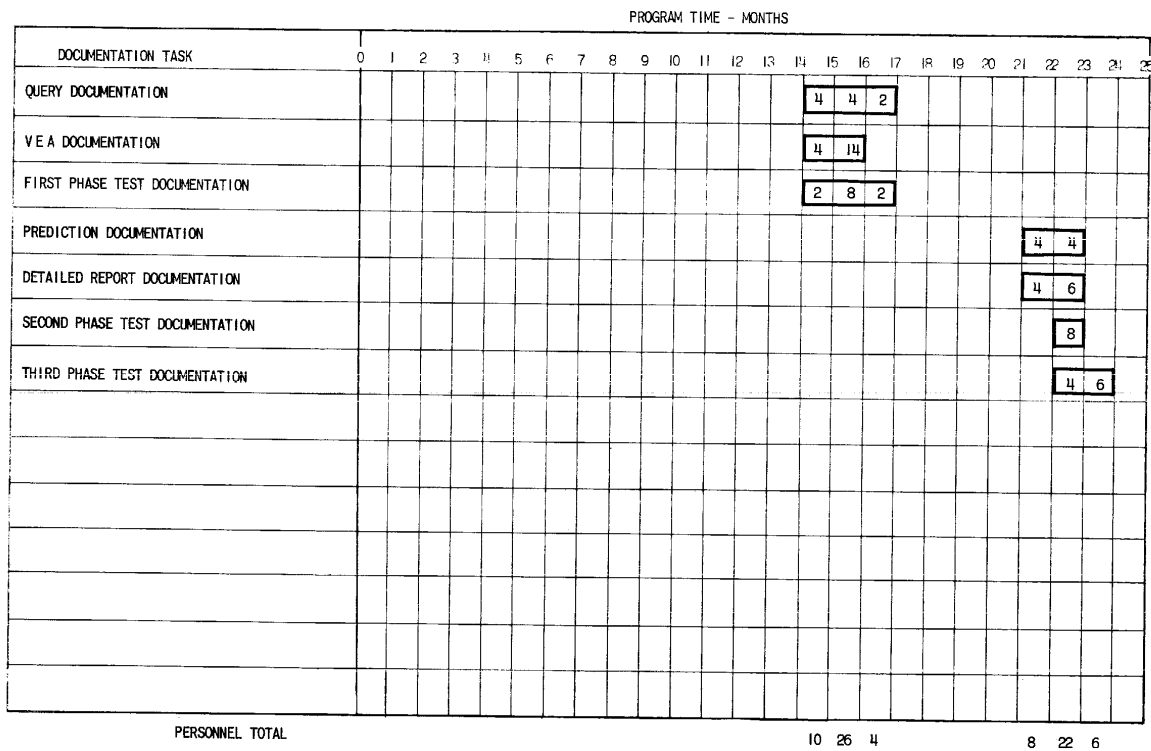


Figure 10 Documentation Schedule

SECRET

SCR 369

#### 4. SYSTEM IMPLEMENTATION COSTS

Cost of system implementation are considered to include the costs of (1) operating the Program Office, (2) preparing, testing and documenting the necessary computer programs and, (3) procuring and installing new equipment. A summary of these costs, on a monthly basis during the 24-month implementation period is provided in Table II. Personnel cost estimates are based on required man-months and typical Contractor rates. Costs for data-base development and training have not been considered for the reasons given in Section 4.4 below.

##### 4.1 Program Office

As was stated in Section 3.0, manpower loadings for the Program Office are a matter of Center organization and policy and the required effort may be divided among a number of organizational elements. We have, however, estimated a monthly dollar cost for the maintenance of such an office, as described in Section 2, based on experience in the implementation of other systems and again using typical Contractor rates.

##### 4.2 Acquisition of Software

The estimates for contract personnel costs in software development, testing, and system installation are based on the IIS design specified in the Final Report and the implementation schedule contained in Section 3.

##### 4.3 Acquisition of Hardware

The summary of equipment costs in Table II makes no allowance for potential credit for the "trade-in" value of existing equipment no longer used. There are two reasons for this: first, the amount and value of such equipment is comparatively small and, second, there appears to be an excellent possibility that much of it might be directed to other purposes within the Center or retained in support of manual backup procedures.

The major peak in the expenditure rate occurs in the eleventh month. This is directly caused by the fact that almost all major items of purchased equipment are installed at that time in preparation for the Category II and Category III testing that must precede the First Operational Phase which begins in the fourteenth month.

The equipment requirements of the IIS include UNIVAC 494 computer equipment already in inventory, new computer equipment which must be acquired, and consoles of various types. Equipment already in inventory which will be employed in the IIS design is not considered as an IIS implementation cost factor. The cost for new computer equipment and

SECRET

25X1A

Approved For Release 2002/09/04 : CIA-RDP78B04747A001900050001-6

Approved For Release 2002/09/04 : CIA-RDP78B04747A001900050001-6

SECRET

SCR 369

consoles are shown in Table III. Equipment costs are shown either as purchase prices or as monthly rental costs. In either case, monthly maintenance costs are shown as separate items.

#### 4.4 Data Base Development and Training

The requirements for data base development and training may or may not be chargeable as IIS implementation expense. The development of plans for these activities, the automatic conversion of parts of the current records into IIS format, and the acquisition and/or preparation of training manuals are costed in the estimates of personnel costs for these Program Office functions, but operational personnel will be required in additional data base conversion activities and the conduct of training (instructor and student time). These additional personnel have not been charged to IIS implementation costs because:

1. Data base conversion to meet the requirements of the NTP is required in any case and will be accomplished as a routine Center operation. The definition of the conversion required must await COMIREX identification of the content and required retrieval capabilities of the National Data Base.
2. Training could be accomplished as an OJT effort. Decision as to the method of training to be employed may be affected by existing operational requirements.

SECRET



25X1A

Approved For Release 2002/09/04 : CIA-RDP78B04747A001900050001-6

Approved For Release 2002/09/04 : CIA-RDP78B04747A001900050001-6

**SECRET**

## APPENDIX A

## SELECTION OF IIS IMPLEMENTATION PLAN

The operational implementation of a system of the size of the IIS must necessarily take into account the available annual funding levels, and within the limits established by these levels provide for at least partial operational capability as quickly as the required components can be installed and tested.

Furthermore, the order in which the partial capabilities are made operational should be responsive to the user's most critical requirements. The order of implementation presented in this plan evolved from a series of discussions between [ ] personnel and the NPIC Technical Monitor and his staff and provided for the following:

- a) The initial operational capabilities of the system should support COMIREX by establishing the IDF as an operationally usable data base.
- b) The ability to obtain information from this data base using the IIS Query capability should be established next.
- c) The system should then grow to encompass the entire spectrum of capabilities described in the system design.

The discussions also resulted in the definition of three additional factors to be taken into account during implementation planning:

- a) The manpower required to staff the Program Office was not to be directly considered.
- b) The number of personnel to be utilized in programming and associated tasks was to remain essentially constant over the entire implementation period.
- c) The IDF capability should be available within a time span of less than one year.

Within these ground rules, the Contractor agreed to consider three different modes of operation of the central computer complex, all of which would provide the required IDF capability in the desired time span.

Mode I is the simplest case and establishes the IDF as a tape file which would be operated upon using techniques available under the TIPS system.

A-1

**SECRET**

SECRET

SCR 369

Mode II places the IDF on a random access storage device (e.g., Fastrand II drum) and operates against the file using batched queries under the RUM/ART system.

Mode III uses the same type of storage as Mode II for the IDF but operates against the file using the real-time techniques designed for the IIS.

Implementation schedules were then developed for all three modes in sufficient detail to permit estimates to be made of the total manpower and elapsed time required, and to ascertain if any significant implementation problems would exist.

A summary of the results of the further investigation of three modes is given in Tables A-I and A-II. Table A-I shows how the operation at NPIC would be affected if different central processor modes were selected. The System Characteristics listed are those that would exist between the time of the Initial IDF capabilities and the time of the 1st Operational Phase. The significance of the entries in Table A-II is described in the following paragraphs.

Mode I - It was determined that a time period of approximately 10 months would be required to develop the IDF capability under TIPS. In order to do this, approximately 12 people would be required. If these 12 people continued to be employed in developing the IIS, the total implementation would require approximately 74 months. It was also ascertained that significant amounts of software developed during the first 10 months of the program would no longer be applicable when the IDF was transferred to the Drum Storage devices of the IIS and would have to be redone. The assignment of additional personnel to the development of the system in this mode appeared to be unwise since a version of Mode II could be developed with 16 people.

Mode II - With 16 people as the minimum number (Mode II Slow), an IDF capability could be developed under ART in approximately 10.5 months. These 16 people could successfully implement the entire IIS in approximately 52 months. In this mode, it appears that approximately 4 percent of the total implementation effort would be expended in developing computer programs and operational procedures which would not be used in the operational IIS.

Increasing the manpower to 28 people during the development activities (Mode II Fast) could shorten the entire IIS development time to about 30 months. The utilization of more than 28 people did not seem justified in view of the fact that the development of the IIS under Mode III would be more efficient if 36 people were available.

A-2

SECRET

TABLE A-I  
SYSTEM CHARACTERISTICS AT TIME OF INITIAL IDF CAPABILITIES

	MODE				
	<u>I</u>	<u>II Slow and Fast</u>	<u>III Slow</u>	<u>III Fast</u>	<u>III Modified</u>
Presentations	BLIPS	BLIPS	BLIPS	IIS	IIS
I and II Reports	Old System	Old System	Old System	IIS <sup>1</sup>	IIS
Prediction	Strips	Strips	Strips	Strips	Strips
IDF	Tape	Drum	Drum	Drum	Drum
Queries	Batched Under TIPS	Batched Under ART	IIS	IIS	IIS
Worksheets	Old Form	Intermediate <sup>2</sup> Worksheet	Intermediate <sup>2</sup> Worksheet	IIS Worksheet	IIS Worksheet
Field Reports	Old Form	Old Form	Old Form	New <sup>1</sup>	IIS Worksheet
Data Entry	826	826	826	IIS Data Entry <sup>1</sup>	IIS Data Entry
Update	Reconvert <sup>2</sup>	Reconvert <sup>2</sup> Changed Rec'ds	IIS	IIS	IIS
Data Deletion	Reconvert <sup>2</sup>	Reconvert <sup>2</sup> Changed Rec'ds	IIS	IIS	IIS

## NOTES:

<sup>1</sup> Within two months of IDF Capability

<sup>2</sup> Temporary technique to solve operational necessities

TABLE A-II  
MANPOWER LOADING AND TIMING OF CAPABILITIES

	MODE					
	<u>I</u>	<u>II Slow</u>	<u>II Fast</u>	<u>III Slow</u>	<u>III Fast</u>	<u>III Modified</u>
Software Personnel	12	16	28	36	50	36
Timing (months from start of program)						
IDF Capability	10	11	11	11	11	14
IIS Query Capability	--	22	17	11	11	14
1st Operational Phase	--	34	20	22	13	14
2nd Operational Phase	--	46	28	23	16	22
3rd Operational Phase	74	52	30	23	16	24

SECRET

A-4

SECRET

SCR 369

Mode III - With 36 people developing the IIS under the Mode III Slow concept, the entire implementation could be completed in approximately 23 months. The IDF capability and the IIS Query capability would be available at 11 months and the remainder of the operational capabilities near the end of the development cycle. The addition of more people (Mode III Fast) would speed up the completion of the development cycle.

The apparent inconsistency between the timing of the first Operational Phase under Modes II Fast and III Slow is caused by the effects on III Slow of the constraint that the IDF capability be available in less than one year. It was agreed to investigate the effect on Mode III Slow of relaxing this constraint. The result of the investigation is shown on Figure A-II as "Mode III Modified." This indicates that, with 36 people, the IDF capability and the first Operational Phase could be made available in 14 months. The more rapid implementation of the first Operational Phase poses considerable difficulty in maintaining a completely level manpower allocation and causes a one month extension of the program. This extension however requires no additional development effort because somewhat less than the specified 36 people are to be used in the last 8 months.\* The total development manpower costs for all three Mode III systems are the same. In view of this fact, it was agreed with the Technical Monitor that Mode III Modified should be expanded to become the Detailed Implementation Plan for the IIS.

\* See Table II - Page 34

SECRET

APPENDIX B

IMPLEMENTATION REQUIREMENTS PLANNING SHEETS

This appendix contains a reproduction of the basic Implementation Requirements Planning Sheets utilized in deriving the schedules of Section 3 of this report and the CPM material of Appendix C. These forms also act as a cross reference between the implementation plan and the IIS system design as described in Part I, Volume 2, of the system design report.

B-1

SECRET

IMPLEMENTATION REQUIREMENTS PLANNING SHEET						
IMPLEMENTATION GROUP		Prediction (Pre-Readout Activity)				SHEET ___ OF ___
ACTIVITY NUMBER		SYSTEM	SYSTEM	CLOCK TIME (DAYS)	RELATIVE COST	
START	STOP	PROCESS NUMBER	PROCESS NAME			
320	420	1.1.1.X	Determine Coverage Rectangles	126		
420	600	1.1.2.X	Coverage Prediction			
320	440	1.1.7.X	Coordinate Prediction	84		
320	460	1.1.8.X	Target Can Number Match	42		
		1.1.9.X	Sort List by Pass Coordinate Order			
0	240	1.1.10.X	Generate Status List	21		
0	300	None	Strips Method	42		

25X1A

SECRET

SCR 369



IMPLEMENTATION REQUIREMENTS PLANNING SHEET

IMPLEMENTATION REQUIREMENTS PLANNING SHEET

IMPLEMENTATION GROUP		Data Entry		SHEET ____ OF ____	
ACTIVITY NUMBER		SYSTEM	SYSTEM	CLOCK TIME (DAYS)	RELATIVE COST
START	STOP	PROCESS NUMBER	PROCESS NAME		
0	180	1.4.1.X	Add Target to Queue List	42	
0	280	1.4.2.X	Enter Readout in W. F. & Change Status	147	
		1.4.3.X	Insert Information		
320	400	2.2.1.X	Create Basic Report Working File	63	
400	500	3.3.1.X	Select Reports for Data Base Update		

25X1A

SECRET

SCR 369

SECRET

B-3

**SECRET**

25X1A

**SECRET**

SCR 369

[illegible]

Approved For Release 2002/09/04 : CIA-RDP78B04747A001900050001-6

IMPLEMENTATION REQUIREMENTS PLANNING SHEET

IMPLEMENTATION GROUP		Photo Reference File		SHEET ____ OF ____	
ACTIVITY NUMBER		SYSTEM	SYSTEM	CLOCK	RELATIVE
START	STOP	PROCESS NUMBER	PROCESS NAME	TIME (DAYS)	COST
0	230	None	Pull from the Position 1° Square Index by Mission & Pass	42	
0	230	None	Place M & P # in 1° Square Index and Merge	21	
0	230	None	Determine Area Coverage by 1° Squares	42	
0	230	None	Pull entries from Photo Reference File	21	
0	230	None	From MPF Pull Ephemeris Data	21	
0	230	None	Do fine Calculation and pull frame #'s	63	

SECRET

B-5

25X1A

SECRET

SCR 369

Approved For Release 2002/09/04 : CIA-RDP78B04747A001900050001-6

IMPLEMENTATION REQUIREMENTS PLANNING SHEET

IMPLEMENTATION GROUP		Special One Time Programs		SHEET ____ OF ____	
ACTIVITY NUMBER		SYSTEM	SYSTEM	CLOCK TIME (DAYS)	RELATIVE COST
START	STOP	PROCESS NUMBER	PROCESS NAME		
0	120	None	Develop Program To Convert TBF Baskets To IDF Sectors	42	
120	160	None	Develop Program To Convert TBF Header Tape Into IDF Header Sector	21	
0	240	None	Develop Program To Accept Keyed in Target Data To Be Used in Presentation Generation	42	

25X1A

SECRET

SCR 369

Approved For Release 2002/09/04 : CIA-RDP78B04747A001900050001-6

SECRET

B-6

IMPLEMENTATION REQUIREMENTS PLANNING SHEET

IMPLEMENTATION GROUP		Miscellaneous Utility		Sheet ____ OF ____	
ACTIVITY NUMBER		SYSTEM	SYSTEM	CLOCK TIME (DAYS)	RELATIVE COST
START	STOP	PROCESS NUMBER	PROCESS NAME		
0	170	None	Utility  Initial Loader  Backup Loader	42	
0	170	None	Periodic Update  Repack Fastrands Update Master Tape Purge Random Access Maintain Index Records	105	
0	170	None	Backup  Drum to Drum to Tape  Transaction Tape for use with Master Tape Load	105	

25X1A

SECRET

SCR 369

B-7  
SECRET

**SECRET**

25X1A

**SECRET**

SCR 369

IMPLEMENTATION GROUP				Automatic Update		SHEET ____ OF ____	
ACTIVITY NUMBER		SYSTEM	SYSTEM	CLOCK TIME (DAYS)	RELATIVE COST		
START	STOP	PROCESS NUMBER	PROCESS NAME				
0	190	3.1.3.X 3.1.4.X	Create File Add Data For File	126			
0	190	3.1.5.X 3.1.6.X	Delete Data Modify Index	147			

Approved For Release 2002/09/04 : CIA-RDP78B04747A001900050001-6

IMPLEMENTATION REQUIREMENTS PLANNING SHEET

IMPLEMENTATION GROUP		File Control		Sheet ____ OF ____	
ACTIVITY NUMBER		SYSTEM	SYSTEM	CLOCK TIME (DAYS)	RELATIVE COST
START	STOP	PROCESS NUMBER	PROCESS NAME		
0	190	None	Control Access To: National Data Base Queue List Working File	252	<input type="text"/>

SECRET

B-9

25X1A

SECRET

SCR 369

Approved For Release 2002/09/04 : CIA-RDP78B04747A001900050001-6

IMPLEMENTATION REQUIREMENTS PLANNING SHEET

IMPLEMENTATION GROUP		VEA		SHEET ____ OF ____	
ACTIVITY NUMBER		SYSTEM	SYSTEM	CLOCK	RELATIVE
START	STOP	PROCESS NUMBER	PROCESS NAME	TIME (DAYS)	COST
0	200	1.4.4.X	Verify Displayed Readout	210	
		1.4.5.X	Edit Verified Readout		
		1.4.6.X	Approve Edit Readout		
		1.4.7.X	Select Data for Data Base		
320	400	2.2.2.X	Verify Entered Material	63	
		2.2.3.X	Edit Verified Material		
		2.2.4.X	Approve Edit Material		
		2.2.5.X	Select Material for Data Base		
400	500				

25X1A

SECRET

SCR 369

SECRET

B-10

Approved For Release 2002/09/04 : CIA-RDP78B04747A001900050001-6



IMPLEMENTATION REQUIREMENTS PLANNING SHEET

IMPLEMENTATION GROUP		Query Language		SHEET ____ OF ____	
ACTIVITY NUMBER		SYSTEM	SYSTEM	CLOCK TIME (DAYS)	RELATIVE COST
START	STOP	PROCESS NUMBER	PROCESS NAME		
0	160	3.2.5.X	Display to User	294	
160	250	3.2.3.X	Decode Query		
		3.2.4.X	Retrieve Required Information		
320	560	3.2.6.X	Route to COINS Switch	63	

25X1A

SECRET

SCR 369

SECRET

B-11

Approved For Release 2002/09/04 : CIA-RDP78B04747A001900050001-6

[illegible]

25X1A

**SECRET**

SCR 369

**SECRET**

B-12

Approved For Release 2002/09/04 : CIA-RDP78B04747A001900050001-6

## IMPLEMENTATION REQUIREMENTS PLANNING SHEET

IMPLEMENTATION GROUP		Report Generation		SHEET ____ OF ____	
ACTIVITY NUMBER		SYSTEM	SYSTEM	CLOCK	RELATIVE
START	STOP	PROCESS NUMBER	PROCESS NAME	TIME (DAYS)	COST
0	220	1.8.1.X	Sort Status List Into Report Order	210	
		1.8.2.X	Extract Sterile Targets		
		1.8.3.X	Generate Index		
		1.8.4.X	Assemble Text		
		1.8.5.X	Edit Text		
		1.8.6.X	Prepare Mats for PSD		
320	380	1.8.7.X	Assemble Cable Version	42	
320	400	2.3.1.X	Change Selective Sections of Report	63	
400	500	2.3.2.X	Prepare Proof Copy of Text	63	
		2.3.4.X	Prepare Mats and Store Report Text		
380	680	1.5.X	Cable Text Preparation	42	

25X1A

SECRET

SCR 369

Approved For Release 2002/09/04 : CIA-RDP78B04747A001900050001-6

IMPLEMENTATION REQUIREMENTS PLANNING SHEET

IMPLEMENTATION GROUP		Computation Support Package (Assignment)		SHEET ___ OF ___	
ACTIVITY NUMBER		SYSTEM	SYSTEM	CLOCK TIME (DAYS)	RELATIVE COST
START	STOP	PROCESS NUMBER	PROCESS NAME		
320	460	1.1.3.X	Sort Phase I and Phase II Targets	42	
460	600	1.1.12.X	Film Can Assignment		
320	540	1.1.4.X	Maintain PI Map File	21	
320	520	1.1.5.X 11.13.X	Compute Expected Team Workload Prepare Update Data	42	
0	240	1.1.11.X	Print PI Presentation Sheets	63	

25X1A

SECRET

SCR 369

SECRET

B-14

Approved For Release 2002/09/04 : CIA-RDP78B04747A001900050001-6

IMPLEMENTATION REQUIREMENTS PLANNING SHEET

IMPLEMENTATION GROUP		Test Support (IPD)				SHEET 1 OF 1	
ACTIVITY NUMBER		SYSTEM	SYSTEM	CLOCK TIME (DAYS)	RELATIVE COST		
START	STOP	PROCESS NUMBER	PROCESS NAME				
160	260		Support Query Test	42			
200	280		Support VEA Test	42			
240	300		Support Report Test	42			
161 300	300 320		Support 1 Phase Cat III Test	42			
460 600	600 660		Support Prediction Test	42			
460 620	620 660		Support 2 Phase Cat III Test	63			
400 480	480 700		Support DPIR Test	42			
500 700	680 740		Support 3 Phase Cat III Test	42			

25X1A

SECRET

SCR 369

SECRET

B-15

Approved For Release 2002/09/04 : CIA-RDP78B04747A001900050001-6

IMPLEMENTATION REQUIREMENTS PLANNING SHEET					
IMPLEMENTATION GROUP Documentation Support (IPD)				Sheet 1 of 1	
ACTIVITY NUMBER		SYSTEM	SYSTEM	CLOCK	RELATIVE
START	STOP	PROCESS NUMBER	PROCESS NAME	TIME (DAYS)	COST
260	360		Support Query Documentation	63	
280	360		Support VEA Documentation	42	
300 340	340 360		Support 1 Phase test documentation	63	
600	780		Support Prediction documentation	42	
620	780		Support 2 Phase test documentation	21	
480 720	720 780		Support DPIR test documentation	42	
700 760	760 780		Support 3 Phase test documentation	42	

25X1A

SECRET

CR 369

Approved For Release 2002/09/04 : CIA-RDP78B04747A001900050001-6

IMPLEMENTATION REQUIREMENTS PLANNING SHEET

IMPLEMENTATION GROUP		Hardware Acquisition ( Program Office)		SHEET 1 OF 2	
ACTIVITY NUMBER		SYSTEM	SYSTEM	CLOCK TIME (DAYS)	RELATIVE COST
START	STOP	PROCESS NUMBER	PROCESS NAME		
0	12		Acquire Double Font Edit Consoles	315	
12	13				
13	14				
14	15				
15	200				
0	21		Acquire TTY Receive Only Consoles	189	
21	22				
22	23				
23	24				
24	25				
25	160				
0	31		Acquire TTY Send/Receive Consoles	189	
31	32				
32	33				
33	34				
34	35				
35	160				
0	41		Acquire Query Consoles	252	
41	42				
42	43				
43	44				
44	45				
45	160				
0	55		Acquire Double Font Printer	168	R
55	240				

25X1A

SECRET

SCR 369

SECRET

B-17

Approved For Release 2002/09/04 : CIA-RDP78B04747A001900050001-6

IMPLEMENTATION REQUIREMENTS PLANNING SHEET

IMPLEMENTATION GROUP		Hardware Acquisition (Program Office)		Sheet 2 of 2	
ACTIVITY NUMBER		SYSTEM	SYSTEM	CLOCK	RELATIVE
START	STOP	PROCESS NUMBER	PROCESS NAME	TIME (DAYS)	COST
0	61		Acquire Data Entry Consoles	252	
61	62				
62	63				
63	64				
64	65				
65	161				
0	75		Acquire CTM's (High Speed)	84	
75	161				
0	85		Acquire CTM's (Low Speed)	84	
85	161				
0	95		Acquire 1782 Drums	147	
95	161				
0	391		Acquire TTY Send/Receive/Punch Console	189	
391	392				
392	393				
393	394				
394	395				
395	680				

25X1A

SECRET

SCR 369

Approved For Release 2002/09/04 : CIA-RDP78B04747A001900050001-6

SECRET

B-18



IMPLEMENTATION REQUIREMENTS PLANNING SHEET

IMPLEMENTATION GROUP		Test Plans (Program Office)		SHEET 1 OF 2	
ACTIVITY NUMBER		SYSTEM	SYSTEM	CLOCK TIME (DAYS)	RELATIVE COST
START	STOP	PROCESS NUMBER	PROCESS NAME		
0	110		Prepare overall test plans	231	
0	210				
0	310				
110	160		Perform Category II Query Test Program	189	
110	111				
111	160				
160	260				
260	315				
110	200		Perform Category II VEA Test Program	189	
110	112				
112	200				
200	280				
280	315				
110	240		Perform Category II Report Test Program	189	
240	300				
300	315				
110	300		Perform 1 Phase Category III Test Program	231	
300	320				
320	365				
110	113				
113	300				
210	460		Perform Category II Prediction Test Program	168	
460	600				
600	615				

SECRET

B-19

SECRET

SCR 369

Approved For Release 2002/09/04 : CIA-RDP78B04747A001900050001-6

IMPLEMENTATION REQUIREMENTS PLANNING SHEET					
IMPLEMENTATION GROUP		Test Plans (Program Office)			SHEET 2 OF 2
ACTIVITY NUMBER		SYSTEM	SYSTEM	CLOCK TIME (DAYS)	RELATIVE COST
START	STOP	PROCESS NUMBER	PROCESS NAME		
210 620 660	620 660 665		Perform 2 Phase Category III Test Program	189	
310 480 700	480 700 715		Perform Category II DPIR Test Program	168	
310 700 740	700 740 765		Perform 3 Phase Category III Test Program	210	

SECRET

B-20

SECRET

SCR 369

Approved For Release 2002/09/04 : CIA-RDP78B04747A001900050001-6

IMPLEMENTATION REQUIREMENTS PLANNING SHEET

IMPLEMENTATION GROUP		Training ( Program Office)		SHEET 1 OF 1	
ACTIVITY NUMBER		SYSTEM	SYSTEM	CLOCK	RELATIVE
START	STOP	PROCESS NUMBER	PROCESS NAME	TIME (DAYS)	COST
0	156		Prepare for I Phase personnel training	137	
0	157				
156	158				
157	158				
158	165		Query Training	52	
165	300				
158	205		VEA Training	52	
205	300				
158	245		Report Training	52	
245	300				
0	256		Prepare for 2 Phase personnel	137	
0	257				
256	258				
257	258				
258	465		Prediction Training	52	
465	620				
258	565		COINS Training	52	
565	620				
0	356		Prepare for 3 Phase personnel training	137	
0	357				
356	358				
357	358				
358	485		DPIR Training	52	
485	700				

SECRET

B-21

SECRET

SCR 369

**SECRET**

SCR 369

## APPENDIX C

## APPLICATION OF CPM TO IIS SCHEDULING

This appendix contains an intermeshed set of arrow diagrams as shown in Figures C-1 through C-4 prepared to illustrate the interrelationships between tasks in software development, testing, documentation, procurement and training. In addition, a CPM Run-off of these tasks is supplied as shown in Figures C-5 and C-6.

C-1

**SECRET**

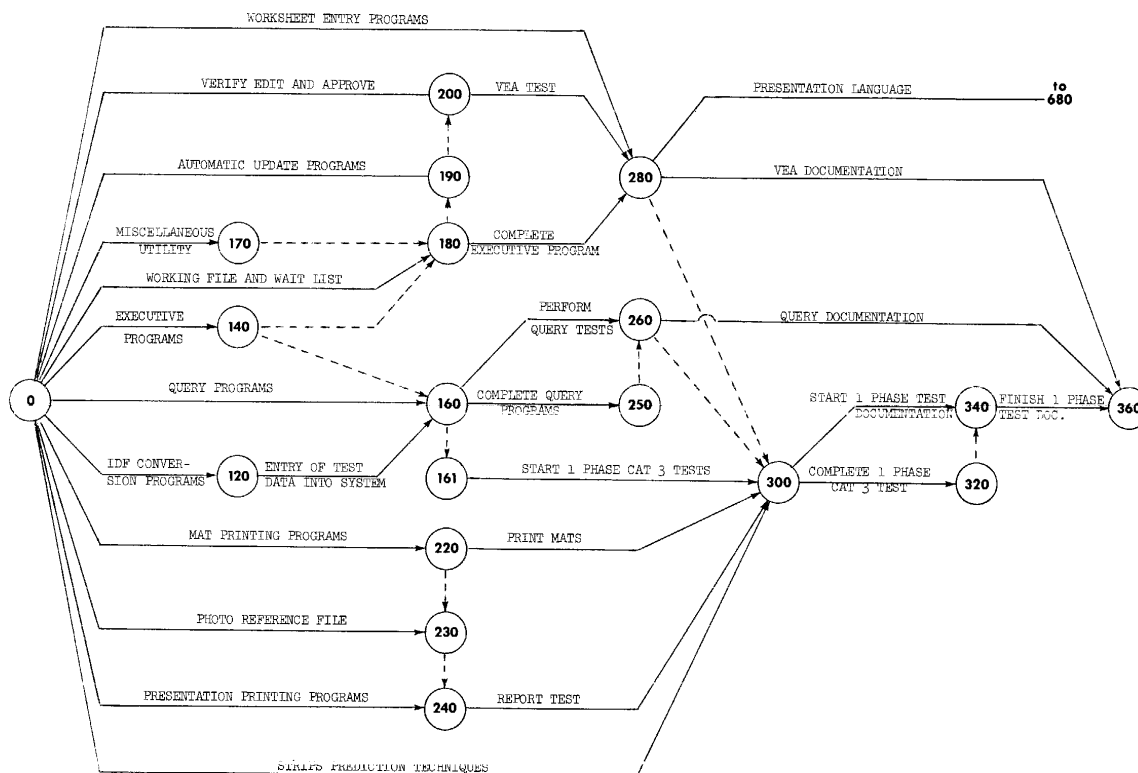


Figure C-1 CPM Arrow Diagram for Programming, Test and Documentation

Sheet 1 of 2

Approved For Release 2002/09/04 : CIA-RDP78B04747A001900050001-6



**SECRET**

Sheet 2 of 2

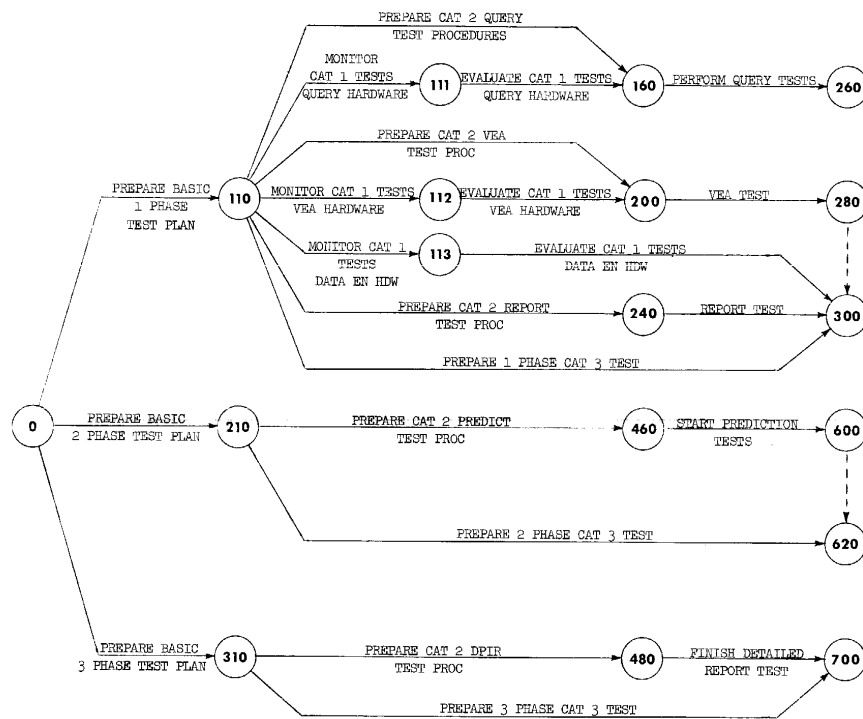


Figure C-2 CPM Arrow Diagram for Tests

Sheet 1 of 2

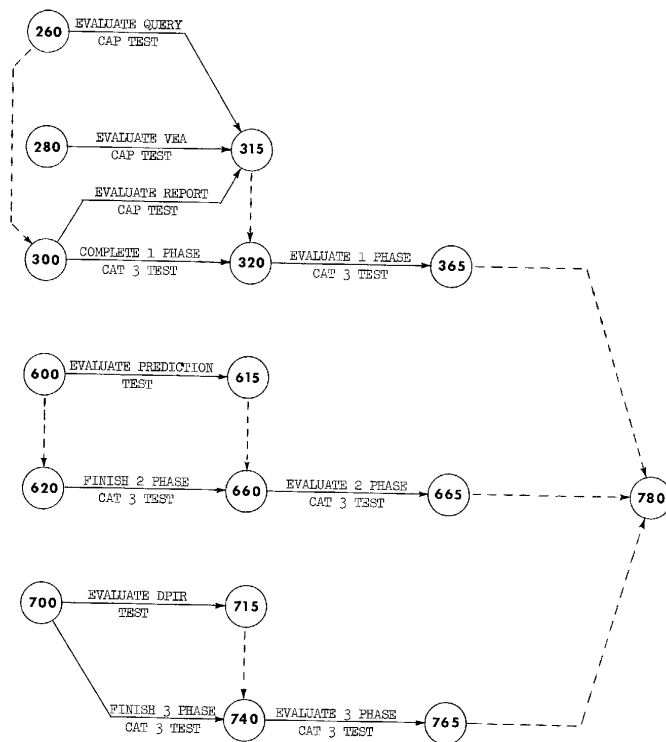


Figure C-2 CPM Arrow Diagram for Tests



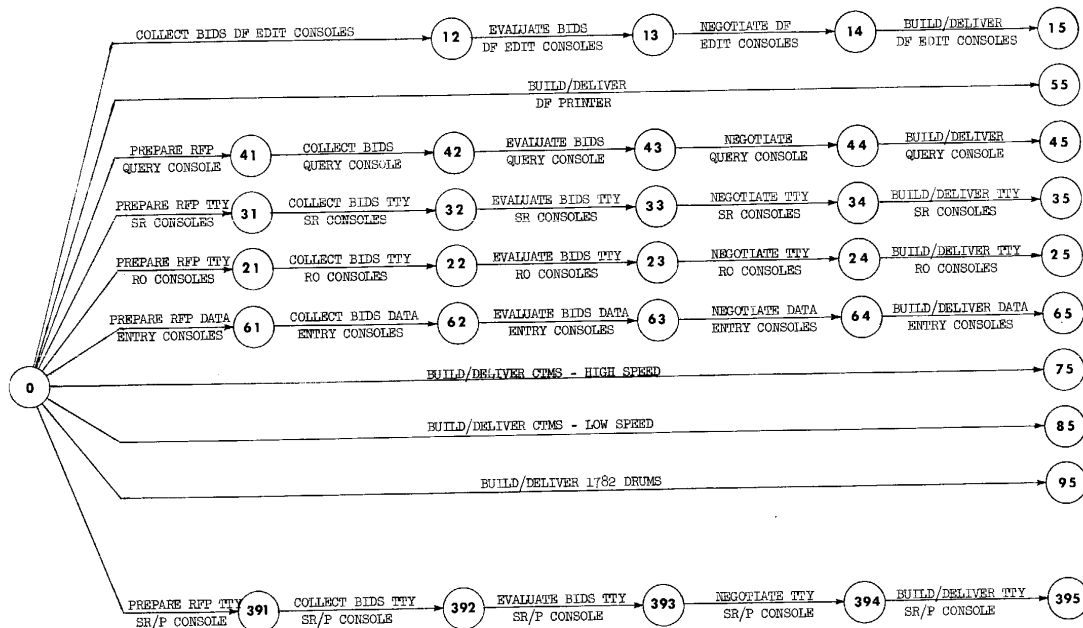


Figure C-3 CFM Arrow Diagram for Hardware Procurement

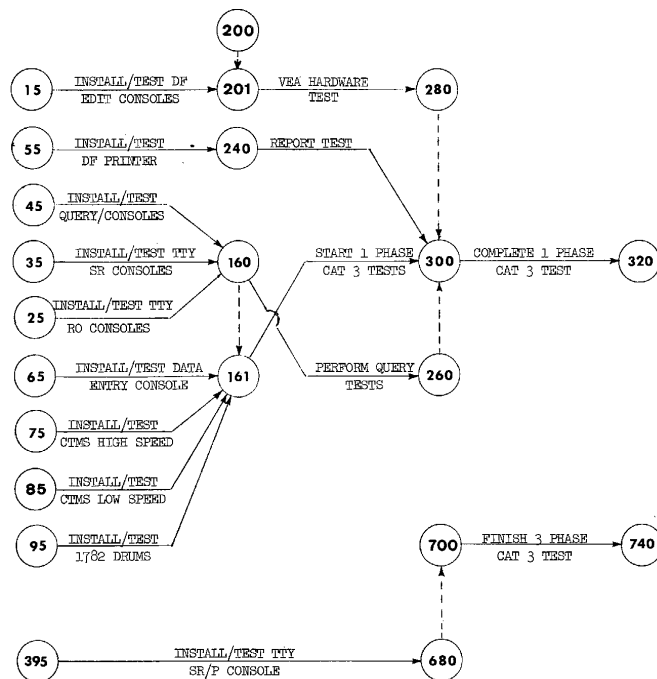


Figure C-3 CPM Arrow Diagram for Hardware Procurement

Sheet 2 of 2

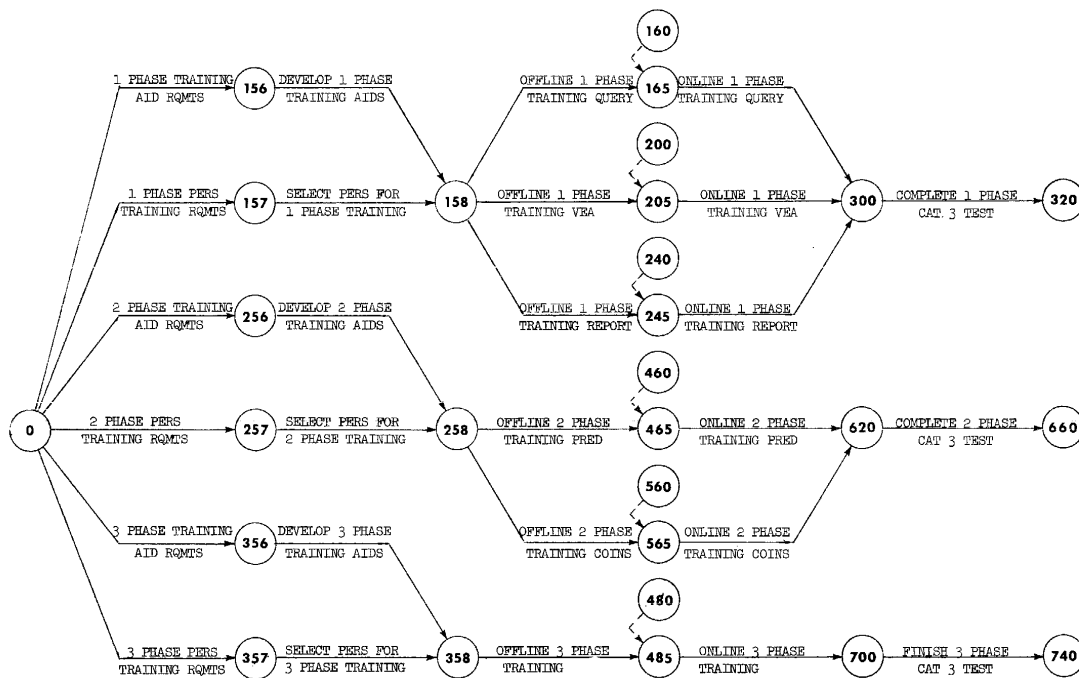


Figure C-4 CPM Arrow Diagram for Training

ACTIVITY	CPM	FOR	IIS	IMPLEMENTATION	EARLIEST	LATEST	TOTAL	FREE
I	J	ACTIVITY	COST	ACTIVITY DESCRIPTION	START	FINISH	FLOAT	FLOAT
0	12	0	0	COLLECT BIDS OF EDIT CONSOLES	0	0	0	0
0	21	11	0	PREPARE RFP TTY RO CONSOLES	0	63	63	0
0	31	11	0	PREPARE RFP TTY SR CONSOLES	0	63	63	0
0	41	11	0	PREPARE RFP QUERY CONSOLES	0	11	0	0
0	55	147	0	BUILD/DELIVER OF PRINTER	0	147	84	0
0	61	11	0	PREPARE RFP DATA ENTRY CONSOLES	0	21	21	0
0	75	63	0	BUILD/DELIVER CTMS-HIGH SPEED	0	63	189	0
0	85	63	0	BUILD/DELIVER CTMS-LOW SPEED	0	63	189	0
0	95	126	0	BUILD/DELIVER 1782 DRUMS	0	126	126	0
0	110	63	0	PREPARE BASIC 1 PHASE TEST PLAN	0	63	63	0
0	120	42	16	IDF CONVERSION PROGRAMS	0	42	178	0
0	140	252	120	EXECUTIVE PROGRAMS	0	252	0	0
0	156	11	0	1 PHASE TRAINING AID RGMTS	0	11	184	115
0	157	5	0	1 PHASE PERS TRAINING RGMTS	0	5	226	231
0	160	252	176	QUERY PROGRAMS	0	252	0	0
0	170	252	88	MISCELLANEOUS UTILITY	0	252	0	0
0	180	63	16	WORKING FILE AND WAIT LIST	0	63	189	189
0	190	210	200	AUTOMATIC UPDATE PROGRAMS	0	210	42	42
0	200	252	90	VERIFY EDIT AND APPROVE	0	252	0	0
0	210	63	0	PREPARE BASIC 2 PHASE TEST PLAN	0	63	231	0
0	220	231	48	MAT PRINTING PROGRAMS	0	231	21	0
0	230	252	56	PHOTO REFERENCE FILE	0	252	0	0
0	240	126	24	PRESENTATION PRINTING PROGRAMS	0	126	126	126
0	256	11	0	2 PHASE TRAINING AID RGMTS	0	11	272	0
0	257	5	0	2 PHASE PERS TRAINING RGMTS	0	5	394	0
0	260	147	32	WORKSHEET ENTRY PROGRAMS	0	147	294	147
0	300	42	8	STRIPS PREDICTION TECHNIQUES	0	42	252	252
0	310	42	0	PREPARE BASIC 3 PHASE TEST PLAN	0	42	294	0
0	356	11	0	3 PHASE TRAINING AID RGMTS	0	11	272	0
0	357	5	0	3 PHASE PERS TRAINING RGMTS	0	5	394	0
0	391	11	0	PREPARE RFP TTY SR/P CONSOLE	0	11	273	273
12	13	32	0	EVALUATE BIDS OF EDIT CONSOLES	32	32	0	0
13	14	31	0	NEGOTIATE OF EDIT CONSOLES	32	63	32	0
14	15	169	391	BUILD/DELIVER OF EDIT CONSOLES	63	252	63	0
15	201	21	0	INSTALL/TEST OF EDIT CONSOLES	252	273	273	0
21	22	31	0	COLLECT BIDS TTY RO CONSOLES	11	42	74	185
22	23	32	0	EVALUATE BIDS TTY RO CONSOLES	42	74	185	137
23	24	31	0	NEGOTIATE TTY RO CONSOLES	74	165	137	168
24	25	63	18	BUILD/DELIVER TTY RO CONSOLES	185	168	231	231
25	160	21	0	INSTALL/TEST TTY RO CONSOLES	168	189	231	252
31	32	31	0	COLLECT BIDS TTY SR CONSOLES	11	42	74	185
32	33	32	0	EVALUATE BIDS TTY SR CONSOLES	42	74	185	137
33	34	31	0	NEGOTIATE TTY SR CONSOLES	74	185	137	168
34	35	63	25	BUILD/DELIVER TTY SR CONSOLES	185	168	231	231
35	160	21	0	INSTALL/TEST TTY SR CONSOLES	168	189	231	252
41	42	31	0	COLLECT BIDS QUERY CONSOLES	11	42	74	185
42	43	32	0	EVALUATE BIDS QUERY CONSOLES	42	74	185	137
43	44	31	0	NEGOTIATE QUERY CONSOLES	74	185	137	168
44	45	126	84	BUILD/DELIVER QUERY CONSOLES	185	231	231	252
45	160	21	0	INSTALL/TEST QUERY CONSOLES	231	252	231	252

Figure C-5. . Output From CPM Calculations Run

Sheet 1 of 4

SECRET

SCR 369

CPM ACTIVITY I	FOR ACTIVITY J	IIS DUR	IMPLEMENTATION COST	ACTIVITY, DESCRIPTION	EARLIEST START	FINISH	LATEST START	FINISH	TOTAL FLOAT	FREE FLOAT
55	246	21	.	INSTALL/TEST OF PRINTER	147	168	231	252	84	84
61	62	31	.	COLLECT BIDS DATA ENTRY CONSOLES	11	42	32	63	21	0
62	63	32	.	EVALUATE BIDS DATA ENTRY CONSOLE	42	74	63	95	21	0
63	64	31	.	NEGOTIATE DATA ENTRY CONSOLES	74	105	95	126	21	0
64	65	126	9.	BUILD/DELIVER DATA ENTRY CONSOLE	105	231	126	252	21	0
65	161	21	.	INSTALL/TEST DATA ENTRY CONSOLE	231	252	252	273	21	0
75	161	21	.	INSTALL/TEST CTMS-HIGH SPEED	63	84	252	273	189	168
85	161	21	.	INSTALL/TEST CTMS-LOW SPEED	63	84	252	273	189	168
95	161	21	.	INSTALL/TEST 1782 DRUMS	126	147	252	273	136	105
110	111	42	.	MONITOR CAT 1 TESTS QUERY HOW	63	185	199	241	136	0
110	112	42	.	MONITOR CAT 1 TESTS VEA HOW	63	185	199	241	136	0
110	113	42	.	MONITOR CAT 1 TESTS DATA EN HOW	63	185	241	263	178	0
110	160	126	.	PREPARE CAT 2 QUERY TEST PROC	63	189	126	252	63	63
110	240	126	.	PREPARE CAT 2 VEA TEST PROC	63	189	126	252	63	63
110	300	168	.	PREPARE CAT 2 REPORT TEST PROC	63	189	126	252	63	63
111	160	11	.	PREPARE 1 PHASE CAT 3 TEST	63	189	126	252	63	63
112	200	11	.	EVALUATE CAT 1 TESTS QUERY HOW	185	231	126	294	63	63
113	300	11	.	EVALUATE CAT 1 TESTS VEA HOW	165	116	241	252	136	136
120	160	0	0.	EVALUATE CAT 1 TESTS DATA EN HOW	185	116	241	252	136	136
140	160	0	0.	ENTRY OF TEST DATA INTO SYSTEM	42	74	283	294	178	178
140	180	0	0.	DUMMY	252	252	220	252	178	178
150	150	126	.	DEVELOP 1 PHASE TRAINING AIDS	252	252	252	252	0	0
157	158	10	.	SELECT PERS FOR 1 PHASE TRAINING	11	137	252	252	0	0
158	165	42	.	OFFLINE 1 PHASE TRAINING	5	15	231	241	104	0
158	205	42	.	OFFLINE 1 PHASE TRAINING QUERY	137	179	241	241	226	122
158	245	42	.	OFFLINE 1 PHASE TRAINING VEA	137	179	241	283	104	73
160	161	0	0.	OFFLINE 1 PHASE TRAINING REPORT	137	179	241	283	104	73
160	165	0	0.	DUMMY	252	252	273	273	104	73
160	250	42	0.	COMPLETE QUERY PROGRAMS	252	252	283	283	21	0
160	260	42	24.	PERFORM QUERY TESTS	252	294	252	294	31	0
161	300	21	0.	START 1 PHASE CAT 3 TESTS	252	294	252	294	0	0
165	300	11	.	ONLINE 1 PHASE TRAINING QUERY	252	273	273	294	21	21
170	180	0	0.	DUMMY	252	263	283	294	31	31
180	190	0	0.	DUMMY	252	252	252	252	0	0
180	200	42	24.	COMPLETE EXECUTIVE PROGRAM	252	252	252	252	0	0
190	200	0	0.	DUMMY	252	252	252	252	0	0
200	201	0	0.	DUMMY	252	252	252	252	0	0
200	205	0	0.	DUMMY	252	252	252	252	0	0
200	200	42	24.	VEA TEST	252	252	273	273	21	21
201	200	21	.	VEA HARDWARE TEST	252	294	283	283	31	0
205	300	11	.	ONLINE 1 PHASE TRAINING VEA	273	294	252	294	0	0
210	400	126	.	PREPARE CAT 2 PREDICT TEST PROC	252	263	273	294	0	0
210	620	147	.	PREPARE 2 PHASE CAT 3 TEST	63	189	294	294	31	31
220	230	0	0.	DUMMY	63	210	315	420	231	231
220	300	42	32.	PRINT MATS	231	231	252	252	252	252
230	240	0	0.	DUMMY	231	273	252	252	21	21
240	245	0	0.	DUMMY	252	252	252	252	21	21
240	300	42	0.	REPORT TEST	252	252	283	283	0	0
245	300	11	0.	ONLINE 1 PHASE TRAINING REPORT	252	294	252	294	31	0
					252	263	283	294	0	0
							283	294	31	31

Figure C-5. Output From CPM Calculations Run

Sheet 2 of 4

SECRET

C-10

SECRET

SCR 369

ACTIVITY	CPM	FOR	IIS	IMPLEMENTATION	ACTIVITY, DESCRIPTION	EARLIEST	LATEST	TOTAL	FREE
I	J	DUR	COST			START	FINISH	FLOAT	FLOAT
250	260	0	•	DUMMY		294	294	0	0
256	250	126	•	DEVELOP 2 PHASE TRAINING AIDS		11	137	272	122
257	250	10	•	SELECT PERS FOR 2 PHASE TRAINING		5	15	399	241
258	465	42	•	OFFLINE 2 PHASE TRAINING PRED		137	179	272	199
258	565	42	•	OFFLINE 2 PHASE TRAINING COINS		137	179	0	0
260	300	0	•	DUMMY		294	294	0	0
260	315	21	•	EVALUATE QUERY CAP TEST		294	315	147	0
260	360	63	20	QUERY DOCUMENTATION		294	357	0	0
280	300	0	•	DUMMY		294	294	0	0
280	315	21	•	EVALUATE VEA CAP TEST		294	315	168	21
280	360	42	36	VEA DOCUMENTATION		294	336	0	0
280	680	168	92	PRESENTATION LANGUAGE		294	462	0	0
300	315	21	•	EVALUATE REPORT CAP TEST		294	315	0	0
300	320	21	42	COMPLETE 1 PHASE CAT 3 TEST		294	315	147	0
300	340	21	4	START 1 PHASE TEST DOCUMENTATION		42	108	273	252
310	480	126	•	PREPARE CAT II DPIR TEST PROC		42	210	252	0
310	780	168	•	PREPARE 3 PHASE CAT 3 TEST		315	315	0	0
315	320	0	•	DUMMY		315	315	147	0
320	340	0	•	DUMMY		315	336	168	0
320	365	21	•	EVALUATE 1 PHASE CAT 3 TEST		315	357	63	0
320	380	42	8	CABLE VERSION PROGRAM		315	399	21	0
320	480	84	52	START BPIR VEA PROGRAM		315	420	0	21
320	420	185	48	START COVERAGE PREDICTION		315	399	42	42
320	440	84	48	COORDINATE PREDICTION		315	378	73	0
320	460	63	24	TARGET/CAN MATCH PROGRAM		315	378	115	42
320	520	63	16	TEAM WORKLOADS PROGRAMS		315	336	73	0
320	540	21	4	MAP FILE PROGRAMS		315	378	147	0
320	560	63	12	COINS SWITCH PROGRAMS		315	357	272	0
340	360	42	20	FINISH 1 PHASE TEST DOC		11	137	394	122
356	350	126	•	DEVELOP 3 PHASE TRAINING AIDS		5	15	272	241
357	350	18	•	SELECT PERS FOR 3 PHASE TRAINING		137	179	147	147
358	485	42	•	OFFLINE 3 PHASE TRAINING		357	357	168	168
360	780	0	•	DUMMY		336	336	63	63
365	780	0	•	DUMMY		357	399	273	0
380	680	42	8	IMMEDIATE CABLE PROGRAMS		11	42	273	0
391	392	31	•	COLLECT BIDS TTY SR/P CONSOLE		42	74	273	0
392	393	32	•	EVALUATE BIDS TTY SR/P CONSOLE		74	185	273	0
393	394	31	•	NEGOTIATE TTY SR/P CONSOLE		185	168	441	273
394	395	63	5	BUILD/DELIVER TTY SR/P CONSOLE		168	189	441	273
395	680	21	•	INSTALL/TEST TTY SR/P CONSOLE		399	420	441	21
400	480	21	8	START DETAILED REPORT TEST		399	420	441	0
400	500	21	4	FINISH BPIR VEA PROGRAM		420	420	21	0
420	440	0	•	DUMMY		420	441	0	0
420	680	21	12	FINISH COVERAGE PREDICTION		420	420	31	0
440	460	0	•	DUMMY		420	451	21	0
440	465	0	•	DUMMY		420	441	0	0
460	680	21	12	START PREDICTION TESTS		420	462	31	31
460	620	42	8	START 2 PHASE CAT 3 TEST		420	431	0	0
465	620	11	•	ONLINE 2 PHASE TRAINING PRED		420	451	31	0
480	485	0	•	DUMMY		420	420	0	0

Sheet 3 of 4

Figure C-5. Output From CPM Calculations Run

SECRET

SCR 369

CP#	ACTIVITY	FOR	IIS	IMPLEMENTATION	ACTIVITY	DESCRIPTION	EARLIEST	LATEST	TOTAL	FREE
1	2	3	4	5	6	7	8	9	10	11
ACTIVITY	DUR	COST					START	FINISH	START	FINISH
480	500	0	12.	DUMMY			420	420	441	441
480	700	21	12.	FINISH DETAILED REPORT TEST			420	441	441	441
480	720	21	0.	START DETAILED REPORT DOC			420	441	441	441
485	700	11	0.	ONLINE 3 PHASE TRAINING			420	441	462	462
500	600	21	12.	START 3 PHASE CAT 3 TEST			420	431	451	462
520	540	0	0.	DUMMY			420	441	441	462
540	500	0	0.	DUMMY			378	378	451	451
560	500	0	0.	DUMMY			378	378	451	451
560	620	0	0.	DUMMY			378	378	451	451
565	620	11	0.	DUMMY			378	378	451	451
600	615	21	0.	ONLINE 2 PHASE TRAINING COINS			378	378	451	451
600	620	0	0.	EVALUATE PREDICTION TEST			378	378	451	451
600	660	21	0.	DUMMY			441	462	451	462
600	700	42	4.	FINISH PREDICTION TEST			441	441	462	462
615	660	0	20.	PREDICTION DOCUMENTATION			441	462	462	462
620	660	21	0.	DUMMY			441	462	462	462
620	700	21	12.	FINISH 2 PHASE CAT 3 TEST			462	462	483	483
660	665	21	10.	2 PHASE TEST DOCUMENTATION			462	462	483	483
660	700	0	0.	EVALUATE 2 PHASE CAT 3 TEST			462	483	483	483
665	700	0	0.	DUMMY			483	504	504	504
680	700	0	0.	DUMMY			483	504	504	504
700	715	21	0.	EVALUATE DPIR TEST			462	462	462	462
700	720	0	0.	DUMMY			462	483	462	483
700	740	21	20.	FINISH 3 PHASE CAT 3 TEST			462	462	483	483
715	740	0	0.	START 3 PHASE TEST DOC			462	483	483	483
720	740	21	0.	DUMMY			462	483	483	483
740	700	0	0.	FINISH DETAILED REPORT DOC			462	483	483	483
740	765	0	0.	DUMMY			483	483	483	483
760	700	21	0.	EVALUATE 3 PHASE CAT 3 TEST			483	483	504	504
765	700	21	12.	FINISH 3 PHASE TEST DOC			483	483	504	504
760	790	0	0.	DUMMY			504	504	504	504
PROJECT COST	2140.			DUMMY			504	504	504	504
				PROJECT COMPLETION			504	504	504	504

Figure C-5. Output From CPM Calculations Run

Sheet 4 of 4

SECRET

C-12

SECRET

FOR 369

CPM FOR IIS IMPLEMENTATION				5 DAY WORKWEEK								TOTAL	FREE	
ACTIVITY	ACTIVITY	ACTIVITY	ACTIVITY	ACTIVITY DESCRIPTION	START	EARLIEST	FINISH	START	LATEST	FINISH	FINISH	FINISH	FLOAT	FLOAT
1	J	DUR	COST											
0	12	0	.	COLLECT BIDS DF EDIT CONSOLES	JAN 1968	JAN 1968	JAN 1968	JAN 1968	JAN 1968	JAN 1968	JAN 1968	JAN 1968	0	0
0	21	11	.	PREPARE RFP TTY RO CONSOLES	JAN 1968	JAN 1668	MAR 2968	APR 1568	JAN 1968	JAN 1968	JAN 1968	JAN 1968	63	0
0	31	11	.	PREPARE RFP TTY SR CONSOLES	JAN 1968	JAN 1668	MAR 2968	APR 1568	JAN 1968	JAN 1968	JAN 1968	JAN 1968	63	0
0	41	11	.	PREPARE RFP QUERY CONSOLES	JAN 1968	JAN 1668	MAR 2968	APR 1568	JAN 1968	JAN 1968	JAN 1968	JAN 1968	63	0
0	55	147	.	BUILD/DELIVER DF PRINTER	JAN 1968	JUL 2968	APR 2968	NOV 2568	JAN 1968	JAN 1968	JAN 1968	JAN 1968	84	0
0	61	11	.	PREPARE RFP DATA ENTRY CONSOLES	JAN 1968	JAN 1668	JAN 3068	FEB 1468	JAN 1968	JAN 1968	JAN 1968	JAN 1968	21	0
0	75	63	.	BUILD/DELIVER CTMS-HIGH SPEED	JAN 1968	MAR 2968	SEP 2668	DEC 2668	JAN 1968	JAN 1968	JAN 1968	JAN 1968	129	0
0	85	63	.	BUILD/DELIVER CTMS-LOW SPEED	JAN 1968	MAR 2968	SEP 2668	DEC 2668	JAN 1968	JAN 1968	JAN 1968	JAN 1968	189	0
0	95	126	.	BUILD/DELIVER 1782 DRUMS	JAN 1968	JUN 2768	JUN 2768	DEC 2668	JAN 1968	JAN 1968	JAN 1968	JAN 1968	126	0
0	118	63	.	PREPARE BASIC 1 PHASE TEST PLAN	JAN 1968	MAR 2968	MAR 2968	JUN 2768	JAN 1968	JAN 1968	JAN 1968	JAN 1968	63	0
0	120	42	16.	IDF CONVERSION PROGRAMS	JAN 1968	FEB 2968	SEP 1168	NOV 768	JAN 1968	JAN 1968	JAN 1968	JAN 1968	178	0
0	140	252	120.	EXECUTIVE PROGRAMS	JAN 1968	DEC 2668	JAN 1968	DEC 2668	JAN 1968	JAN 1968	JAN 1968	JAN 1968	0	0
0	150	11	.	1 PHASE TRAINING AID RGMTS	JAN 1968	JAN 1668	MAY 2768	JUN 1268	JAN 1968	JAN 1968	JAN 1968	JAN 1968	184	0
0	157	5	.	1 PHASE PERS TRAINING RGMTS	JAN 1968	JAN 868	NOV 1868	NOV 2568	JAN 1968	JAN 1968	JAN 1968	JAN 1968	226	0
0	160	252	176.	QUERY PROGRAMS	JAN 1968	DEC 2668	JAN 1968	DEC 2668	JAN 1968	JAN 1968	JAN 1968	JAN 1968	0	0
0	170	252	88.	MISCELLANEOUS UTILITY	JAN 1968	DEC 2668	JAN 1968	DEC 2668	JAN 1968	JAN 1968	JAN 1968	JAN 1968	0	0
0	180	63	16.	WORKING FILE AND WAIT LIST	JAN 1968	MAR 2968	SEP 2668	DEC 2668	JAN 1968	JAN 1968	JAN 1968	JAN 1968	189	189
0	190	210	200.	AUTOMATIC UPDATE PROGRAMS	JAN 1968	OCT 2468	FEB 2968	DEC 2668	JAN 1968	JAN 1968	JAN 1968	JAN 1968	42	42
0	200	252	90.	VERIFY EDIT AND APPROVE	JAN 1968	DEC 2668	JAN 1968	DEC 2668	JAN 1968	JAN 1968	JAN 1968	JAN 1968	0	0
0	210	63	.	PREPARE BASIC 2 PHASE TEST PLAN	JAN 1968	MAR 2968	NOV 2568	FEB 2569	JAN 1968	JAN 1968	JAN 1968	JAN 1968	231	0
0	220	231	48.	WAT PRINTING PROGRAMS	JAN 1968	NOV 2568	JAN 3068	DEC 2668	JAN 1968	JAN 1968	JAN 1968	JAN 1968	21	0
0	230	252	56.	PHOTO REFERENCE FILE	JAN 1968	DEC 2668	JAN 1968	DEC 2668	JAN 1968	JAN 1968	JAN 1968	JAN 1968	0	0
0	240	126	24.	PRESENTATION PRINTING PROGRAMS	JAN 1968	JUN 2768	JUN 2768	DEC 2668	JAN 1968	JAN 1968	JAN 1968	JAN 1968	126	126
0	250	11	.	2 PHASE TRAINING AID RGMTS	JAN 1968	JAN 1668	JAN 2369	FEB 769	JAN 1968	JAN 1968	JAN 1968	JAN 1968	272	0
0	257	5	.	2 PHASE PERS TRAINING RGMTS	JAN 1968	JAN 868	JUL 1769	JUL 2469	JAN 1968	JAN 1968	JAN 1968	JAN 1968	394	0
0	280	147	32.	WORKSHEET ENTRY PROGRAMS	JAN 1968	JUL 2968	JUL 2968	FEB 2569	JAN 1968	JAN 1968	JAN 1968	JAN 1968	147	147
0	300	42	0.	STRIPS PREDICTION TECHNIQUES	JAN 1968	FEB 2968	DEC 2668	FEB 2569	JAN 1968	JAN 1968	JAN 1968	JAN 1968	252	252
0	310	42	.	PREPARE BASIC 3 PHASE TEST PLAN	JAN 1968	FEB 2968	DEC 2668	FEB 2569	JAN 1968	JAN 1968	JAN 1968	JAN 1968	252	0
0	350	11	.	3 PHASE TRAINING AID RGMTS	JAN 1968	JAN 1668	JAN 2369	FEB 769	JAN 1968	JAN 1968	JAN 1968	JAN 1968	272	0
0	357	5	.	3 PHASE PERS TRAINING RGMTS	JAN 1968	JAN 868	JUL 1769	JUL 2469	JAN 1968	JAN 1968	JAN 1968	JAN 1968	394	0
0	391	11	.	PREPARE RFP TTY SR/P CONSOLE	JAN 1968	JAN 1668	JAN 2469	FEB 1069	JAN 1968	JAN 1968	JAN 1968	JAN 1968	273	0
12	13	32	.	EVALUATE BIDS DF EDIT CONSOLES	JAN 1968	FEB 1468	JAN 1968	FEB 1468	JAN 1968	JAN 1968	JAN 1968	JAN 1968	0	0
13	14	31	.	NEGOTIATE DF EDIT CONSOLES	FEB 1468	MAR 2968	FEB 1468	MAR 2968	JAN 1968	JAN 1968	JAN 1968	JAN 1968	0	0
14	15	189	391.	BUILD/DELIVER DF EDIT CONSOLES	MAR 2968	DEC 2668	MAR 2968	DEC 2668	JAN 1968	JAN 1968	JAN 1968	JAN 1968	0	0
15	201	21	.	INSTALL/TEST DF EDIT CONSOLES	DEC 2668	JAN 2469	DEC 2668	JAN 2469	JAN 1968	JAN 1968	JAN 1968	JAN 1968	0	0
21	22	31	.	COLLECT BIDS TTY RO CONSOLES	JAN 1968	FEB 2968	APR 1568	MAY 2868	JAN 1968	JAN 1968	JAN 1968	JAN 1968	63	0
22	23	32	.	EVALUATE BIDS TTY RO CONSOLES	FEB 2968	APR 1568	MAY 2868	JUL 1568	JAN 1968	JAN 1968	JAN 1968	JAN 1968	63	0
23	24	31	.	NEGOTIATE TTY RO CONSOLES	APR 1568	MAY 2868	JUL 1568	AUG 2768	JAN 1968	JAN 1968	JAN 1968	JAN 1968	63	0
24	25	63	16.	BUILD/DELIVER TTY RO CONSOLES	MAY 2868	AUG 2768	AUG 2768	NOV 2568	JAN 1968	JAN 1968	JAN 1968	JAN 1968	63	0
25	100	21	.	INSTALL/TEST TTY RO CONSOLES	AUG 2768	SEP 2668	NOV 2568	DEC 2668	JAN 1968	JAN 1968	JAN 1968	JAN 1968	63	63
31	32	31	.	COLLECT BIDS TTY SR CONSOLES	JAN 1968	FEB 2968	APR 1568	MAY 2868	JAN 1968	JAN 1968	JAN 1968	JAN 1968	63	0
32	33	32	.	EVALUATE BIDS TTY SR CONSOLES	FEB 2968	APR 1568	MAY 2868	JUL 1568	JAN 1968	JAN 1968	JAN 1968	JAN 1968	63	0
33	34	31	.	NEGOTIATE TTY SR CONSOLES	APR 1568	MAY 2868	JUL 1568	AUG 2768	JAN 1968	JAN 1968	JAN 1968	JAN 1968	63	0
34	35	63	25.	BUILD/DELIVER TTY SR CONSOLES	MAY 2868	AUG 2768	AUG 2768	NOV 2568	JAN 1968	JAN 1968	JAN 1968	JAN 1968	63	63
35	100	21	.	INSTALL/TEST TTY SR CONSOLES	AUG 2768	SEP 2668	NOV 2568	DEC 2668	JAN 1968	JAN 1968	JAN 1968	JAN 1968	63	63
41	42	31	.	COLLECT BIDS QUERY CONSOLES	JAN 1968	FEB 2968	JAN 1968	FEB 2968	JAN 1968	JAN 1968	JAN 1968	JAN 1968	0	0
42	43	32	.	EVALUATE BIDS QUERY CONSOLES	FEB 2968	APR 1568	FEB 2968	APR 1568	JAN 1968	JAN 1968	JAN 1968	JAN 1968	0	0
43	44	31	.	NEGOTIATE QUERY CONSOLES	APR 1568	MAY 2868	APR 1568	MAY 2868	JAN 1968	JAN 1968	JAN 1968	JAN 1968	0	0
44	45	126	84.	BUILD/DELIVER QUERY CONSOLES	MAY 2868	NOV 2568	MAY 2868	NOV 2568	JAN 1968	JAN 1968	JAN 1968	JAN 1968	0	0
45	100	21	.	INSTALL/TEST QUERY CONSOLES	NOV 2568	DEC 2668	NOV 2568	DEC 2668	JAN 1968	JAN 1968	JAN 1968	JAN 1968	0	0
55	240	21	.	INSTALL/TEST DF PRINTER	JUL 2968	AUG 2768	NOV 2568	DEC 2668	JAN 1968	JAN 1968	JAN 1968	JAN 1968	84	84

Figure C-6. Output From Calendar Dating Run.

Sheet 1 of 4

SECRET

C-13

SECRET

SCR 369



CP: FOR IIS IMPLEMENTATION				5 DAY WORKWEEK								TOTAL	FREE FLOAT	
ACTIVITY I	ACTIVITY J	ACTIVITY DUR	ACTIVITY COST	ACTIVITY DESCRIPTION	EARLIEST START	FINISH	LATEST START	FINISH	START	FINISH	START	FINISH		FLOAT
61	62	31	.	COLLECT BIDS DATA ENTRY CONSOLES	JAN 16/68	FEB 29/68	FEB 14/68	MAR 29/68					21	0
62	63	32	.	EVALUATE BIDS DATA ENTRY CONSOLE	FEB 29/68	APR 15/68	MAR 29/68	MAY 14/68					21	0
63	64	31	.	NEGOTIATE DATA ENTRY CONSOLES	APR 15/68	MAY 28/68	MAY 14/68	JUN 27/68					21	0
64	65	126	9.	BUILD/DELIVER DATA ENTRY CONSOLE	MAY 28/68	NOV 25/68	JUN 27/68	DEC 26/68					21	0
65	161	21	.	INSTALL/TEST DATA ENTRY CONSOLES	NOV 25/68	DEC 26/68	DEC 26/68	JAN 24/69					21	0
75	161	21	.	INSTALL/TEST CTMS-HIGH SPEED	MAR 29/68	APR 29/68	DEC 26/68	JAN 24/69					189	168
85	161	21	.	INSTALL/TEST CTMS-LOW SPEED	MAR 29/68	APR 29/68	DEC 26/68	JAN 24/69					189	168
95	161	21	.	INSTALL/TEST 1762 DRUMS	JUN 27/68	JUL 29/68	DEC 26/68	JAN 24/69					126	105
110	111	42	.	MONITOR CAT 1 TESTS QUERY HDW	MAR 29/68	MAY 28/68	OCT 9/68	DEC 18/68					136	0
110	112	42	.	MONITOR CAT 1 TESTS VEA HDW	MAR 29/68	MAY 28/68	OCT 9/68	DEC 18/68					136	0
110	113	42	.	MONITOR CAT 1 TESTS DATA EN HDW	MAR 29/68	MAY 28/68	DEC 18/68	FEB 7/69					178	0
110	160	126	.	PREPARE CAT 2 QUERY TEST PROC	MAR 29/68	SEP 26/68	JUN 27/68	DEC 26/68					63	63
110	200	126	.	PREPARE CAT 2 VEA TEST PROC	MAR 29/68	SEP 26/68	JUN 27/68	DEC 26/68					63	63
110	240	126	.	PREPARE CAT 2 REPORT TEST PROC	MAR 29/68	SEP 26/68	JUN 27/68	DEC 26/68					63	63
110	300	160	.	PREPARE 1 PHASE CAT 3 TEST	MAR 29/68	NOV 25/68	JUN 27/68	FEB 25/69					63	63
111	160	11	.	EVALUATE CAT 1 TESTS QUERY HDW	MAY 28/68	JUN 13/68	DEC 18/68	DEC 26/68					136	136
112	200	11	.	EVALUATE CAT 1 TESTS VEA HDW	MAY 28/68	JUN 13/68	DEC 18/68	DEC 26/68					136	136
113	300	11	.	EVALUATE CAT 1 TESTS DATA EN HDW	MAY 28/68	JUN 13/68	FEB 7/69	FEB 25/69					178	178
120	160	32	6.	ENTRY OF TEST DATA INTO SYSTEM	FEB 29/68	APR 15/68	NOV 7/68	DEC 26/68					178	178
140	160	0	.	DUMMY	DEC 26/68	DEC 26/68	DEC 26/68	DEC 26/68					0	0
140	180	0	.	DUMMY	DEC 26/68	DEC 26/68	DEC 26/68	DEC 26/68					0	0
150	150	126	.	DEVELOP 1 PHASE TRAINING AIDS	JAN 16/68	JUL 15/68	JUN 12/68	DEC 18/68					104	0
157	150	10	.	SELECT PERS FOR 1 PHASE TRAINING	JAN 8/68	JAN 22/68	NOV 25/68	DEC 10/68					226	122
158	165	42	.	OFFLINE 1 PHASE TRAINING QUERY	JUL 15/68	SEP 12/68	DEC 18/68	FEB 7/69					104	73
158	205	42	.	OFFLINE 1 PHASE TRAINING VEA	JUL 15/68	SEP 12/68	DEC 18/68	FEB 7/69					104	73
158	245	42	.	OFFLINE 1 PHASE TRAINING REPORT	JUL 15/68	SEP 12/68	DEC 18/68	FEB 7/69					104	73
160	161	0	.	DUMMY	DEC 26/68	DEC 26/68	JAN 24/69	JAN 24/69					21	0
160	165	0	.	DUMMY	DEC 26/68	DEC 26/68	JAN 24/69	JAN 24/69					31	0
160	250	42	6.	COMPLETE QUERY PROGRAMS	DEC 26/68	FEB 25/69	DEC 26/68	FEB 25/69					0	0
160	260	42	24.	PERFORM QUERY TESTS	DEC 26/68	FEB 25/69	DEC 26/68	FEB 25/69					0	0
161	300	21	8.	START 1 PHASE CAT 3 TESTS	DEC 26/68	JAN 18/69	JAN 24/69	FEB 25/69					21	21
165	300	11	.	ONLINE 1 PHASE TRAINING QUERY	DEC 26/68	JAN 18/69	FEB 7/69	FEB 25/69					31	31
170	190	0	.	DUMMY	DEC 26/68	DEC 26/68	DEC 26/68	DEC 26/68					0	0
180	190	0	.	DUMMY	DEC 26/68	DEC 26/68	DEC 26/68	DEC 26/68					0	0
180	200	42	24.	COMPLETE EXECUTIVE PROGRAM	DEC 26/68	FEB 25/69	DEC 26/68	FEB 25/69					0	0
190	200	0	.	DUMMY	DEC 26/68	DEC 26/68	DEC 26/68	DEC 26/68					0	0
200	201	0	.	DUMMY	DEC 26/68	DEC 26/68	JAN 24/69	JAN 24/69					21	21
200	205	0	.	DUMMY	DEC 26/68	DEC 26/68	FEB 7/69	FEB 7/69					31	0
200	200	42	24.	VEA TEST	DEC 26/68	FEB 25/69	DEC 26/68	FEB 25/69					0	0
201	200	21	.	VEA HARDWARE TEST	JAN 24/69	FEB 25/69	JAN 24/69	FEB 25/69					0	0
205	300	11	.	ONLINE 1 PHASE TRAINING VEA	DEC 26/68	JAN 18/69	FEB 7/69	FEB 25/69					31	31
210	400	126	.	PREPARE CAT 2 PREDICT TEST PROC	MAR 29/68	SEP 26/68	FEB 25/69	AUG 22/69					231	231
210	620	147	.	PREPARE 2 PHASE CAT 3 TEST	MAR 29/68	OCT 24/68	MAR 26/69	OCT 21/69					252	252
220	230	0	.	DUMMY	NOV 25/68	NOV 25/68	DEC 26/68	DEC 26/68					21	21
220	300	42	32.	PRINT MATS	NOV 25/68	JAN 24/69	DEC 26/68	FEB 25/69					21	21
230	240	0	.	DUMMY	DEC 26/68	DEC 26/68	DEC 26/68	DEC 26/68					0	0
240	245	0	.	DUMMY	DEC 26/68	DEC 26/68	FEB 7/69	FEB 7/69					31	0
240	300	42	6.	REPORT TEST	DEC 26/68	FEB 25/69	DEC 26/68	FEB 25/69					0	0
245	300	11	.	ONLINE 1 PHASE TRAINING REPORT	DEC 26/68	JAN 18/69	FEB 7/69	FEB 25/69					31	31
250	200	0	.	DUMMY	FEB 25/69	FEB 25/69	FEB 25/69	FEB 25/69					0	0
250	250	126	.	DEVELOP 2 PHASE TRAINING AIDS	JAN 16/68	JUL 15/68	FEB 7/69	AUG 7/69					272	0

Figure C-6. Output From Calendar Dating Run

Sheet 2 of 4

SECRET

SCR 369

CPM FOR IIS IMPLEMENTATION				5 DAY WORKWEEK								TOTAL FLOAT	FREE FLOAT
ACTIVITY I	ACTIVITY J	ACTIVITY KUR	COST	ACTIVITY DESCRIPTION	EARLIEST START	FINISH	LATEST START	FINISH					
257	256	10	.	SELECT PERS FOR 2 PHASE TRAINING	JAN 8/68	JAN 22/68	JUL 24/69	AUG 7/69		394	122		
258	465	42	.	OFFLINE 2 PHASE TRAINING PRED	JUL 15/68	SEP 12/68	AUG 7/69	OCT 6/69		272	241		
258	565	42	.	OFFLINE 2 PHASE TRAINING COINS	JUL 15/68	SEP 12/68	AUG 7/69	OCT 6/69		272	199		
260	300	0	.	DUMMY	FEB 25/69	FEB 25/69	FEB 25/69	FEB 25/69		0	0		
260	315	21	.	EVALUATE QUERY CAP TEST	FEB 25/69	MAR 26/69	FEB 25/69	MAR 26/69		0	0		
260	360	63	20.	QUERY DOCUMENTATION	FEB 25/69	MAY 23/69	SEP 22/69	DEC 22/69		147	0		
280	300	0	.	DUMMY	FEB 25/69	FEB 25/69	FEB 25/69	FEB 25/69		0	0		
280	315	21	.	EVALUATE VEA CAP TEST	FEB 25/69	MAR 26/69	FEB 25/69	MAR 26/69		0	0		
280	360	42	36.	VEA DOCUMENTATION	FEB 25/69	APR 24/69	OCT 21/69	DEC 22/69		168	21		
280	680	168	92.	PRESENTATION LANGUAGE	FEB 25/69	OCT 21/69	FEB 25/69	OCT 21/69		0	0		
300	315	21	.	EVALUATE REPORT CAP TEST	FEB 25/69	MAR 26/69	FEB 25/69	MAR 26/69		0	0		
300	320	21	42.	COMPLETE 1 PHASE CAT 3 TEST	FEB 25/69	MAR 26/69	FEB 25/69	MAR 26/69		0	0		
300	340	21	4.	START 1 PHASE TEST DOCUMENTATION	FEB 25/69	MAR 26/69	SEP 22/69	OCT 21/69		147	0		
310	400	126	.	PREPARE CAT II UPIR TEST PROC	FEB 29/68	AUG 27/68	MAR 26/69	SEP 22/69		273	252		
310	700	160	.	PREPARE 3 PHASE CAT 3 TEST	FEB 29/68	OCT 24/68	FEB 25/69	OCT 21/69		252	252		
315	320	0	.	DUMMY	MAR 26/69	MAR 26/69	MAR 26/69	MAR 26/69		0	0		
320	340	0	.	DUMMY	MAR 26/69	MAR 26/69	OCT 21/69	OCT 21/69		147	0		
320	365	21	.	EVALUATE 1 PHASE CAT 3 TEST	MAR 26/69	APR 24/69	NOV 20/69	DEC 22/69		168	0		
320	380	42	8.	CABLE VERSION PROGRAM	MAR 26/69	MAY 23/69	JUN 24/69	AUG 22/69		03	0		
320	400	84	52.	START BPIR VEA PROGRAM	MAR 26/69	JUL 24/69	APR 24/69	AUG 22/69		21	0		
320	420	165	40.	START COVERAGE PREDICTION	MAR 26/69	AUG 22/69	MAR 26/69	AUG 22/69		0	0		
320	440	84	40.	COORDINATE PREDICTION	MAR 26/69	JUL 24/69	APR 24/69	AUG 22/69		21	21		
320	460	63	24.	TARGET/CAN MATCH PROGRAM	MAR 26/69	JUN 24/69	MAY 23/69	AUG 22/69		42	42		
320	520	63	16.	TEAM WORKLOADS PROGRAMS	MAR 26/69	JUN 24/69	JUL 9/69	OCT 6/69		73	0		
320	540	21	4.	MAP FILE PROGRAMS	MAR 26/69	APR 24/69	SEP 5/69	OCT 6/69		115	42		
320	560	63	12.	COINS SWITCH PROGRAMS	MAR 26/69	JUN 24/69	JUL 9/69	OCT 6/69		73	0		
340	360	42	20.	FINISH 1 PHASE TEST DOC	MAR 26/69	MAY 23/69	OCT 21/69	DEC 22/69		147	0		
350	350	126	.	DEVELOP 3 PHASE TRAINING AIDS	JAN 16/68	JUL 15/68	FEB 7/69	AUG 7/69		272	0		
357	350	10	.	SELECT PERS FOR 3 PHASE TRAINING	JAN 8/68	JAN 22/68	JUL 24/69	AUG 7/69		394	122		
358	465	42	.	OFFLINE 3 PHASE TRAINING	JUL 15/68	SEP 12/68	AUG 7/69	OCT 6/69		272	241		
360	700	0	.	DUMMY	MAY 23/69	MAY 23/69	DEC 22/69	DEC 22/69		147	147		
365	700	0	.	DUMMY	APR 24/69	APR 24/69	DEC 22/69	DEC 22/69		168	168		
380	680	42	0.	IMMEDIATE CABLE PROGRAMS	MAY 23/69	JUL 24/69	AUG 22/69	OCT 21/69		63	63		
391	392	31	.	COLLECT BIDS TTY SR/P CONSOLE	JAN 16/68	FEB 29/68	FEB 10/69	MAR 26/69		273	0		
392	393	32	.	EVALUATE BIDS TTY SR/P CONSOLE	FEB 29/68	APR 15/68	MAR 26/69	MAY 9/69		273	0		
393	394	31	.	NEGOTIATE TTY SR/P CONSOLE	APR 15/68	MAY 20/68	MAY 9/69	JUN 24/69		273	0		
394	395	63	5.	BUILD/DELIVER TTY SR/P CONSOLE	MAY 20/68	AUG 27/68	JUN 24/69	SEP 22/69		273	0		
395	680	21	.	INSTALL/TEST TTY SR/P CONSOLE	AUG 27/68	SEP 26/68	SEP 22/69	OCT 21/69		273	273		
400	400	21	0.	START DETAILED REPORT TEST	JUL 24/69	AUG 22/69	AUG 22/69	SEP 22/69		21	0		
400	500	21	0.	FINISH BPIR VEA PROGRAM	JUL 24/69	AUG 22/69	AUG 22/69	SEP 22/69		21	0		
420	440	0	.	DUMMY	AUG 22/69	AUG 22/69	AUG 22/69	AUG 22/69		0	0		
420	600	21	12.	FINISH COVERAGE PREDICTION	AUG 22/69	SEP 22/69	SEP 22/69	OCT 21/69		21	0		
440	460	0	.	DUMMY	AUG 22/69	SEP 22/69	SEP 22/69	OCT 21/69		21	0		
460	465	0	.	DUMMY	AUG 22/69	AUG 22/69	OCT 6/69	OCT 6/69		0	0		
460	600	21	12.	START PREDICTION TESTS	AUG 22/69	SEP 22/69	SEP 22/69	OCT 21/69		31	0		
460	620	42	0.	START 2 PHASE CAT 3 TEST	AUG 22/69	OCT 21/69	AUG 22/69	OCT 21/69		0	0		
465	620	11	.	ONLINE 2 PHASE TRAINING PRED	AUG 22/69	SEP 8/69	OCT 6/69	OCT 21/69		31	31		
480	485	0	.	DUMMY	AUG 22/69	AUG 22/69	OCT 6/69	OCT 6/69		31	0		
480	500	0	.	DUMMY	AUG 22/69	AUG 22/69	SEP 22/69	SEP 22/69		21	0		
480	700	21	12.	FINISH DETAILED REPORT TEST	AUG 22/69	SEP 22/69	SEP 22/69	OCT 21/69		21	21		
480	720	21	0.	START DETAILED REPORT DOC	AUG 22/69	SEP 22/69	OCT 21/69	NOV 20/69		42	21		

Figure C-6. Output From Calendar Dating Run

Sheet 3 of 4

SECRET

SCR 369

CP- FOR IIS IMPLEMENTATION											
ACTIVITY		ACTIVITY		ACTIVITY DESCRIPTION	5 DAY WORKWEEK				TOTAL	FREE	
I	J	LUR	COST		EARLIEST	FINISH	LATEST	FINISH			FLOAT
485	780	11	.	ONLINE 3 PHASE TRAINING	AUG 22/69	SEP 8/69	OCT 6/69	OCT 21/69	31	31	
520	682	21	12.	START 3 PHASE CAT 3 TEST	AUG 22/69	SEP 22/69	SEP 22/69	OCT 21/69	21	21	
520	540	0	.	DUMMY	JUN 24/69	JUN 24/69	OCT 6/69	OCT 6/69	73	0	
540	560	0	.	DUMMY	JUN 24/69	JUN 24/69	OCT 6/69	OCT 6/69	73	0	
560	565	0	.	DUMMY	JUN 24/69	JUN 24/69	OCT 6/69	OCT 6/69	73	0	
560	620	0	.	DUMMY	JUN 24/69	JUN 24/69	OCT 21/69	OCT 21/69	84	84	
565	620	11	.	ONLINE 2 PHASE TRAINING COINS	JUN 24/69	JUL 10/69	OCT 6/69	OCT 21/69	73	73	
600	615	21	.	EVALUATE PREDICTION TEST	SEP 22/69	OCT 21/69	OCT 21/69	NOV 20/69	21	0	
600	620	0	.	DUMMY	SEP 22/69	SEP 22/69	OCT 21/69	OCT 21/69	21	21	
600	660	21	4.	FINISH PREDICTION TEST	SEP 22/69	OCT 21/69	OCT 21/69	NOV 20/69	21	21	
600	780	42	20.	PREDICTION DOCUMENTATION	SEP 22/69	NOV 20/69	OCT 21/69	DEC 22/69	21	21	
615	660	0	.	DUMMY	OCT 21/69	OCT 21/69	NOV 20/69	NOV 20/69	21	21	
620	680	21	12.	FINISH 2 PHASE CAT 3 TEST	OCT 21/69	NOV 20/69	OCT 21/69	NOV 20/69	0	0	
620	780	21	10.	2 PHASE TEST DOCUMENTATION	OCT 21/69	NOV 20/69	NOV 20/69	DEC 22/69	21	21	
660	665	21	.	EVALUATE 2 PHASE CAT 3 TEST	NOV 20/69	DEC 22/69	NOV 20/69	DEC 22/69	0	0	
660	780	0	.	DUMMY	NOV 20/69	NOV 20/69	DEC 22/69	DEC 22/69	21	21	
665	780	0	.	DUMMY	DEC 22/69	DEC 22/69	DEC 22/69	DEC 22/69	0	0	
680	780	0	.	DUMMY	OCT 21/69	OCT 21/69	OCT 21/69	OCT 21/69	0	0	
700	715	21	.	EVALUATE EPIR TEST	OCT 21/69	NOV 20/69	OCT 21/69	NOV 20/69	0	0	
700	720	0	.	DUMMY	OCT 21/69	OCT 21/69	NOV 20/69	NOV 20/69	21	0	
700	740	21	20.	FINISH 3 PHASE CAT 3 TEST	OCT 21/69	NOV 20/69	OCT 21/69	NOV 20/69	0	0	
700	760	21	0.	START 3 PHASE TEST DOC	OCT 21/69	NOV 20/69	OCT 21/69	NOV 20/69	0	0	
715	740	0	.	DUMMY	NOV 20/69	NOV 20/69	NOV 20/69	NOV 20/69	0	0	
720	780	21	0.	FINISH DETAILED REPORT DOC	OCT 21/69	NOV 20/69	NOV 20/69	DEC 22/69	21	21	
740	760	0	.	DUMMY	NOV 20/69	NOV 20/69	NOV 20/69	NOV 20/69	0	0	
740	765	21	.	EVALUATE 3 PHASE CAT 3 TEST	NOV 20/69	DEC 22/69	NOV 20/69	DEC 22/69	0	0	
760	780	21	12.	FINISH 3 PHASE TEST DOC	NOV 20/69	DEC 22/69	NOV 20/69	DEC 22/69	0	0	
765	780	0	.	DUMMY	DEC 22/69	DEC 22/69	DEC 22/69	DEC 22/69	0	0	
780	790	0	.	DUMMY	DEC 22/69	DEC 22/69	DEC 22/69	DEC 22/69	0	0	
PROJECT COST		2140.		PROJECT COMPLETION							

Figure C-6. Output From Calendar Dating Run

Sheet 4 of 4

SECRET

C-16

SECRET

SCR 369

~~SECRET~~

~~SECRET~~
