

~~CONFIDENTIAL~~

24 September 1970

25X1

Attention: Dave D.

Gentlemen:

In accordance with the requirements on [redacted] Task Order No. 33, we are enclosing three (3) copies of the Twenty-Sixth Monthly Letter Report—for the month of August, 1970—covering the IDT Display Program.

25X1

As a part of this report there is, as required, a Financial Status Report covering this same period.

Very truly yours,

25X1

[redacted]
Engineering Department

NLT:bc
Enclosures (3)
CC—Contracting Officer (1 Encl.)

GROUP-1
Excluded from automatic downgrading
and declassification.

~~Regraded~~ ~~Unclassified~~
When separated from
classified enclosures

THIS DOCUMENT CONTAINS INFORMATION AFFECTING THE NATIONAL DEFENSE OF THE UNITED STATES WITHIN THE MEANING OF THE ESPIONAGE LAWS, TITLE 18, U. S. C., SECTIONS 793 AND 794. ITS TRANSMISSION OR THE REVELATION OF ITS CONTENTS IN ANY MANNER TO AN UNAUTHORIZED PERSON IS PROHIBITED BY LAW.

~~CONFIDENTIAL~~

CONFIDENTIAL

No. of pages 3 (FY4)
Copy 4 of 5 Copies

STATUS DATA

ORD # 6583-70

IDT DISPLAY PROGRAM (U)



25X1

Task Order No. 33


Twenty-Sixth Monthly Letter Report

Month of August 1970

THIS DOCUMENT CONTAINS INFORMATION AFFECTING THE
NATIONAL DEFENSE OF THE UNITED STATES: WITHIN THE
MEANING OF THE ESPIONAGE LAWS, TITLE 18, U. S. C.,
SECTIONS 793 AND 794, ITS TRANSMISSION OR THE REVE-
LATION OF ITS CONTENTS IN ANY MANNER TO AN UN-
AUTHORIZED PERSON IS PROHIBITED BY LAW.

GROUP-1

Excluded from automatic downgrading
and declassification.

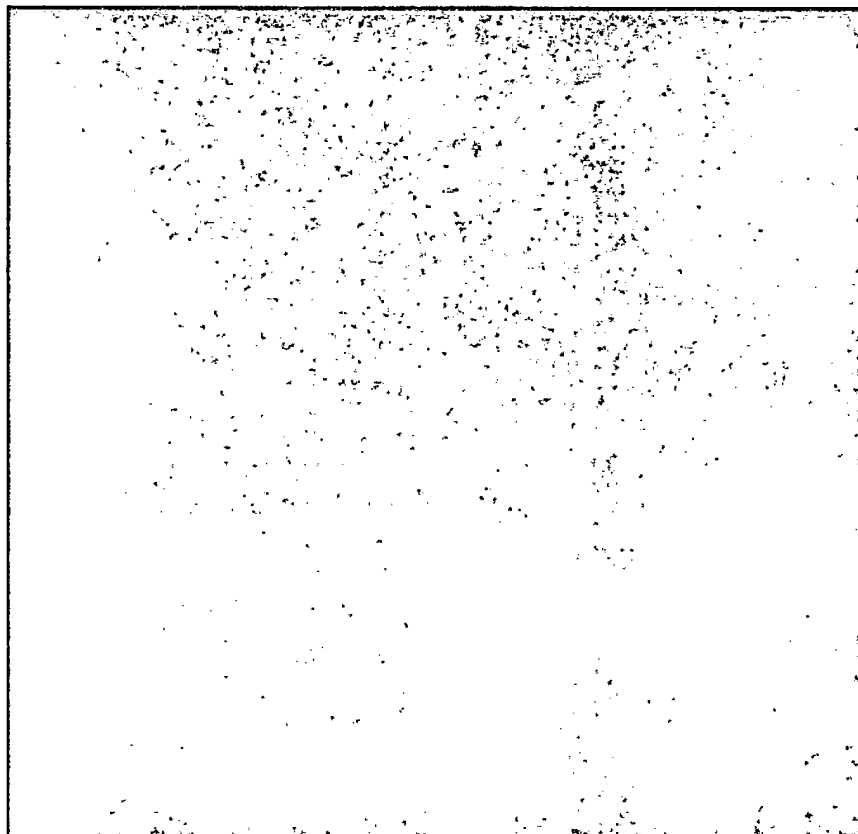

25X1

CONFIDENTIAL

21450

CONFIDENTIAL

25X1

Task No. 33 - 24 June 1968 to 15 Aug. 1970

25X1

Monthly Contract Status ReportFinancial StatusFor Period 1 August 1970 to 29 September 1970

	<u>Target Cost</u>	<u>Target Fee</u>	<u>Target Total</u>
Amount of Contract:	<div></div>		
Amount of Obligations and/ or Expenditures This Period:	<div></div>		
Amount of Obligations and/ or Expenditures to Date:	<div></div>		
Estimated Funds to Complete:			
Percentage of Funds Expended to Date:	93%		
Percentage of Work Completed to Date:	96%		
1. Is work on schedule?		No	
2. Can work be completed in authorized time?		No	
3. Can contract be completed with authorized funds?		Yes	

25X1

25X1

PROJECT STATUS

All major areas have been debugged and system tests have been started. Several small problems uncovered during the tests are being corrected concurrently.

The present test schedule does not allow sufficient time to completely exercise the system. A request for contract extension is being prepared and will be submitted shortly. The remaining funds appear to be sufficient to complete the project.

WORK PLANNED DURING NEXT REPORTING PERIOD

Continue system testing.

CONFIDENTIAL

Page Denied

ORD # 6584-70

TECHNICAL REPORT

IDT DISPLAY PROGRAM (U)




25X1

Task Order No. 33

Twenty-Sixth Monthly Letter Report

Month of August 1970

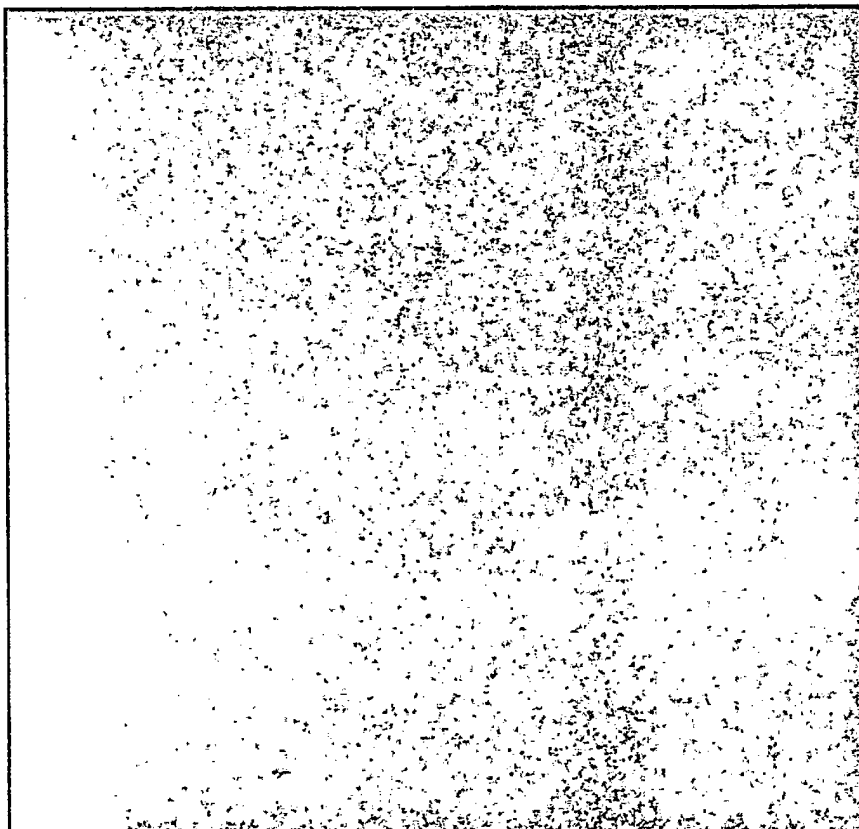

25X1

TECHNICAL REPORT

The software debugging has been completed and testing started.

Several small problems have appeared since the start of testing. These include occasionally erratic operation of the disc write circuitry. The problem appears to stem from noise and should be correctable by proper filtering of the disc write lines.

Several software errors have been detected. The most serious was a shortage of core memory. The problem was alleviated by consolidating several buffer areas and making them relocatable. Other software errors include improper specification of record length in the SCAN routine.
